








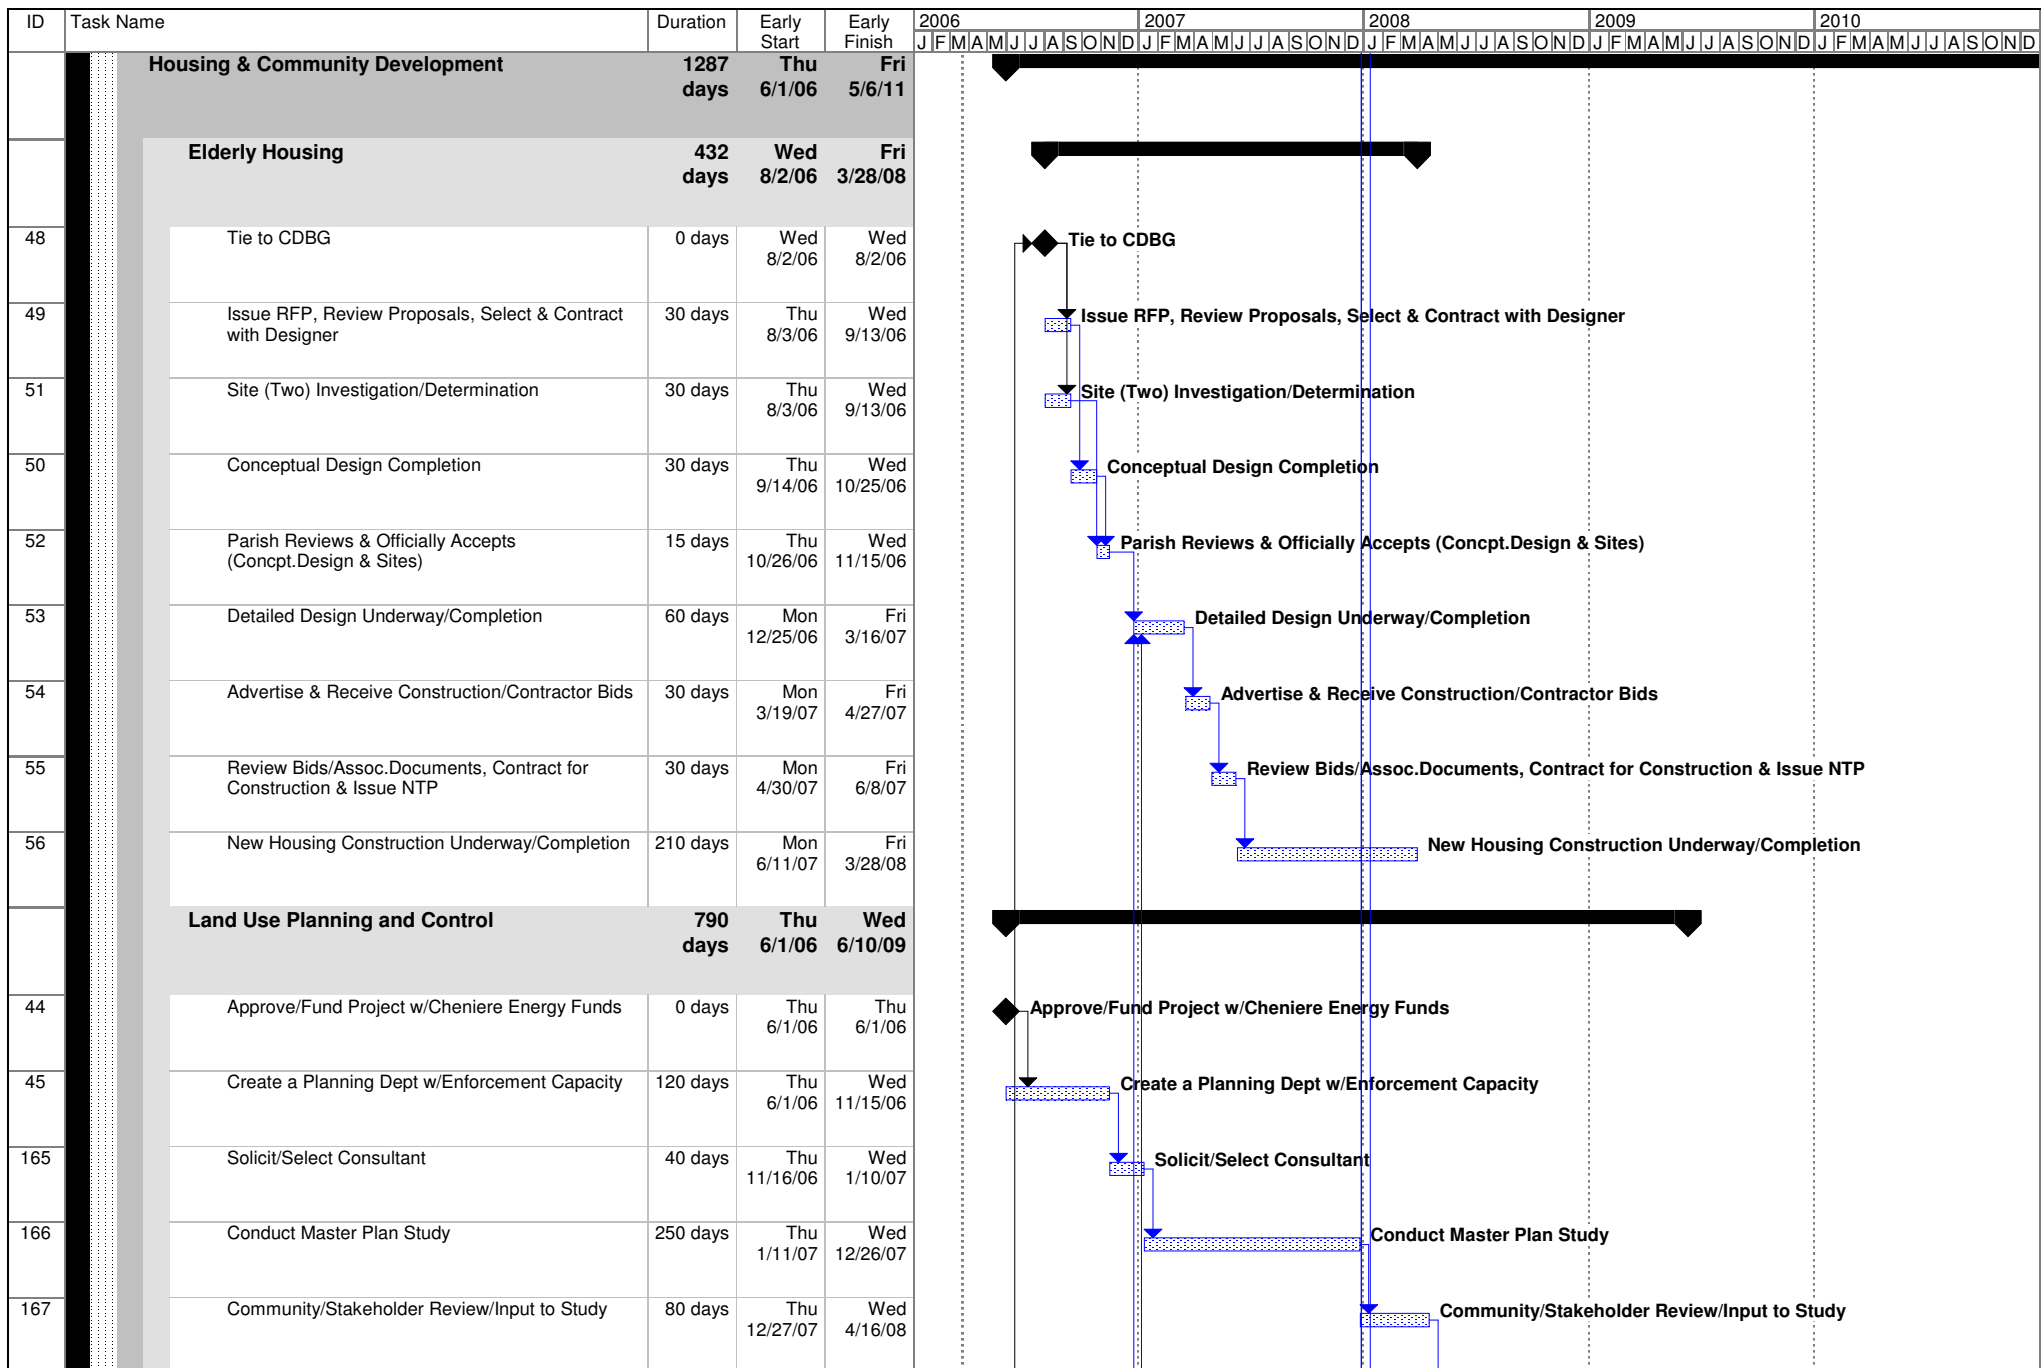


ID	Task Name	Duration	Early Start	Early Finish	2006	2007	2008	2009	2010
					JFMAMJJJASON	DJFMAMJJJASON	DJFMAMJJJASON	DJFMAMJJJASON	DJFMAMJJJASON
31	Revegetate Land Mine Reclamation Sites	40 days	Mon 9/22/08	Fri 11/14/08					
	Coastal Erosion Protection & Restoration	2762 days	Tue 10/31/06	Wed 5/31/17					
70	Authorize/Fund Breakwater	0 days	Tue 10/31/06	Tue 10/31/06					
71	Construct Breakwater at Rockefeller WR	239 days	Tue 10/31/06	Fri 9/28/07					
72	Design FY08 Section of Breakwater	60 days	Tue 10/31/06	Mon 1/22/07					
73	FY08Section of Breakwater	262 days	Mon 10/1/07	Tue 9/30/08					
74	Design FY09 Section of Breakwater	60 days	Mon 10/1/07	Fri 12/21/07					
75	Construct FY09 Section of Breakwater	261 days	Wed 10/1/08	Wed 9/30/09					
76	Design/Construct Remaining Breakwater	2000 days	Thu 10/1/09	Wed 5/31/17					
	Monitoring Elevations in Cameron Parish	300 days	Mon 1/2/06	Fri 2/23/07					
162	Monitoring Elevations in Cameron Parish	300 days	Mon 1/2/06	Fri 2/23/07					
	Post-Event Storm Emergency Action Plans	90 days	Mon 5/1/06	Fri 9/1/06					
21	Receive Approval/Funding for Post-Event Storm Water Management Planning	0 days	Mon 5/1/06	Mon 5/1/06					
22	Review/Revise Existing USCOE Emergency Action Plan	30 days	Mon 5/1/06	Fri 6/9/06					
23	Perform Stakeholder Review of Post-Event Storm Water Management Planning	30 days	Mon 5/1/06	Fri 6/9/06					
24	Integrate USCOE/Stakeholder Input to Plan	30 days	Mon 6/12/06	Fri 7/21/06					
25	Approval/Adoption of Plan	30 days	Mon 7/24/06	Fri 9/1/06					



ID	Task Name	Duration	Early Start	Early Finish	2006 JFMAMJJASOND	2007 JFMAMJJASOND	2008 JFMAMJJASOND	2009 JFMAMJJASOND	2010 JFMAMJJASOND
46	Draft a Land Use Ordance	120 days	Thu 2/21/08	Wed 8/6/08					
168	Present Master Plan to Parish Council/Revise Per Direction	80 days	Thu 4/17/08	Wed 8/6/08					
47	Create a Map of Land Uses	120 days	Thu 8/7/08	Wed 1/21/09					
199	Land Use Planning and Controls Operations	100 days	Thu 1/22/09	Wed 6/10/09					
	Rebuild and Repair Cameron Housing	1200 days	Sat 9/30/06	Fri 5/6/11					
39	501-C-3 Housing Department Establishment Approval of Project	0 days	Sat 9/30/06	Sat 9/30/06					
40	501-C-3 Documentation of Govt Entity Eligibility/Funding Approval	20 days	Mon 10/2/06	Fri 10/27/06					
41	501-C-3 Housing Department Advertise/Hire Employees	40 days	Mon 10/30/06	Fri 12/22/06					
42	Identify/Obtain Financing for Replace/Repair Owner Occupied and Rental Housing	60 days	Mon 12/25/06	Fri 3/16/07					
43	Repair/Replace Owner Occupied and Rental Housing	1080 days	Mon 3/19/07	Fri 5/6/11					
	Public Safety	624 days	Mon 5/1/06	Thu 9/18/08					
	Auxiliary Parish Operations Center (APOC)	556 days	Wed 8/2/06	Thu 9/18/08					
169	Tie to CDBG	0 days	Wed 8/2/06	Wed 8/2/06					
170	Approve/Fund Project	0 days	Wed 8/2/06	Wed 8/2/06					
171	Issue RFP, Review Proposals, Select & Contract with Designer	40 days	Fri 9/1/06	Thu 10/26/06					
172	Alternate Site Investigation/Determination	20 days	Fri 10/27/06	Thu 11/23/06					
174	Parish Reviews & Officially Accepts (Concpt.Design & Altern.Site - If Reconstructing)	15 days	Fri 11/24/06	Thu 12/14/06					










Project: GameSRT Date: Mon 3/20/06	Task		Progress		Summary		External Tasks		Deadline	
	Split		Milestone		Project Summary		External Milestone			

ID	Task Name	Duration	Early Start	Early Finish
173	Conceptual Design Completion - APOC	60 days	Fri 12/15/06	Thu 3/8/07
175	Detailed Design Underway/Completion	120 days	Fri 3/9/07	Thu 8/23/07
176	Advertise & Receive Construction/Contractor Bids	20 days	Fri 8/24/07	Thu 9/20/07
177	Review Bids/Assoc.Documents, Contract for Construction & Issue NTP	20 days	Fri 9/21/07	Thu 10/18/07
178	Construct APOC	240 days	Fri 10/19/07	Thu 9/18/08
	Cameron Parish Justice & Government Center	462 days	Wed 8/2/06	Fri 5/9/08
65	Tie to CDBG	0 days	Wed 8/2/06	Wed 8/2/06
66	Issue RFP, Review Proposals, Select & Contract with Designer	30 days	Fri 9/1/06	Thu 10/12/06
68	Alternate Site Investigation/Determination	30 days	Fri 9/1/06	Thu 10/12/06
67	Conceptual Design Completion	30 days	Fri 10/13/06	Thu 11/23/06
69	Parish Reviews & Officially Accepts (Concpt.Design & Altern.Site - If Reconstructing)	15 days	Fri 11/24/06	Thu 12/14/06
77	Detailed Design Underway/Completion	90 days	Mon 12/25/06	Fri 4/27/07
78	Advertise & Receive Construction/Contractor Bids	30 days	Mon 4/30/07	Fri 6/8/07
79	Review Bids/Assoc.Documents, Contract for Construction & Issue NTP	30 days	Mon 6/11/07	Fri 7/20/07
80	Justice Center Construction Underway/Completion	210 days	Mon 7/23/07	Fri 5/9/08
	Grand Lake Drinking Water Capacity	225 days	Mon 5/1/06	Fri 3/9/07
200	Approve/Fund Project	0 days	Mon 5/1/06	Mon 5/1/06

The Gantt chart displays the following tasks and their durations:

- Conceptual Design Completion - APOC**: 60 days (Fri 12/15/06 to Thu 3/8/07)
- Detailed Design Underway/Completion**: 120 days (Fri 3/9/07 to Thu 8/23/07)
- Advertise & Receive Construction/Contractor Bids**: 20 days (Fri 8/24/07 to Thu 9/20/07)
- Review Bids/Assoc.Documents, Contract for Construction & Issue NTP**: 20 days (Fri 9/21/07 to Thu 10/18/07)
- Construct APOC**: 240 days (Fri 10/19/07 to Thu 9/18/08)
- Cameron Parish Justice & Government Center**: 462 days (Wed 8/2/06 to Fri 5/9/08)
- Tie to CDBG**: 0 days (Wed 8/2/06)
- Issue RFP, Review Proposals, Select & Contract with Designer**: 30 days (Fri 9/1/06 to Thu 10/12/06)
- Alternate Site Investigation/Determination**: 30 days (Fri 9/1/06 to Thu 10/12/06)
- Conceptual Design Completion**: 30 days (Fri 10/13/06 to Thu 11/23/06)
- Parish Reviews & Officially Accepts (Concpt.Design & Altern.Site - If Reconstructing)**: 15 days (Fri 11/24/06 to Thu 12/14/06)
- Detailed Design Underway/Completion**: 90 days (Mon 12/25/06 to Fri 4/27/07)
- Advertise & Receive Construction/Contractor Bids**: 30 days (Mon 4/30/07 to Fri 6/8/07)
- Review Bids/Assoc.Documents, Contract for Construction & Issue NTP**: 30 days (Mon 6/11/07 to Fri 7/20/07)
- Justice Center Construction Underway/Completion**: 210 days (Mon 7/23/07 to Fri 5/9/08)
- Grand Lake Drinking Water Capacity**: 225 days (Mon 5/1/06 to Fri 3/9/07)
- Approve/Fund Project**: 0 days (Mon 5/1/06)

ID	Task Name	Duration	Early Start	Early Finish	2006	2007	2008	2009	2010																															
	LA 27 Shoulder and Roadway Improvements	460 days	Sat 4/1/06	Fri 1/4/08	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
90	Authorize/Fund Improvements (LA 27 East Side)	0 days	Sat 4/1/06	Sat 4/1/06	Authorize/Fund Improvements (LA 27 East Side)																																			
101	Approve/Fund LA 27 Scenic Turnouts (Scenic Turnouts)	0 days	Sat 4/1/06	Sat 4/1/06	Approve/Fund LA 27 Scenic Turnouts (Scenic Turnouts)																																			
105	Approve/Fund Improvements (LA 27 West Side)	0 days	Sat 4/1/06	Sat 4/1/06	Approve/Fund Improvements (LA 27 West Side)																																			
91	Silicate/Award Design Consultant (LA 27 East Side)	30 days	Mon 4/3/06	Fri 5/12/06	Silicate/Award Design Consultant (LA 27 East Side)																																			
92	Negotiate with Land Owner for Right of Way (LA 27 East Side)	30 days	Mon 4/3/06	Fri 5/12/06	Negotiate with Land Owner for Right of Way (LA 27 East Side)																																			
102	Solicit Consultant to Identify Locations/Amenities (Scenic Turnouts)	30 days	Mon 4/3/06	Fri 5/12/06	Solicit Consultant to Identify Locations/Amenities (Scenic Turnouts)																																			
106	Silicate/Award Design Consultant (LA 27 West Side)	30 days	Mon 4/3/06	Fri 5/12/06	Silicate/Award Design Consultant (LA 27 West Side)																																			
93	Design N/S or N Only Shoulder Improvements (LA 27 East Side)	60 days	Mon 5/15/06	Fri 8/4/06	Design N/S or N Only Shoulder Improvements (LA 27 East Side)																																			
94	Environmental Review (LA 27 East Side)	90 days	Mon 5/15/06	Fri 9/15/06	Environmental Review (LA 27 East Side)																																			
103	Select Consultant (Scenic Turnouts)	30 days	Mon 5/15/06	Fri 6/23/06	Select Consultant (Scenic Turnouts)																																			
107	Perform Preliminary Design (LA 27 West Side)	60 days	Mon 5/15/06	Fri 8/4/06	Perform Preliminary Design (LA 27 West Side)																																			
109	Refuge Review of Preliminary Design (LA 27 West Side)	60 days	Mon 5/15/06	Fri 8/4/06	Refuge Review of Preliminary Design (LA 27 West Side)																																			
104	Perform Study/Identify Turnouts for Incorporation into Hwy Designs (Scenic Turnouts)	30 days	Mon 6/26/06	Fri 8/4/06	Perform Study/Identify Turnouts for Incorporation into Hwy Designs (Scenic Turnouts)																																			
108	Tie to LA 27 Scenic Turnouts (LA 27 West Side)	0 days	Fri 8/4/06	Fri 8/4/06	Tie to LA 27 Scenic Turnouts (LA 27 West Side)																																			
110	Environmental Review of Preliminary Design (LA 27 West Side)	30 days	Mon 8/7/06	Fri 9/15/06	Environmental Review of Preliminary Design (LA 27 West Side)																																			
95	Tie to Scenic Turnout Design (LA 27 East Side)	0 days	Fri 8/18/06	Fri 8/18/06	Tie to Scenic Turnout Design (LA 27 East Side)																																			

Project: CameSRT Date: Mon 3/20/06	Task		Progress		Summary		External Tasks		Deadline	
	Split		Milestone		Project Summary		External Milestone			

ID	Task Name	Duration	Early Start	Early Finish	2006	2007	2008	2009	2010
96	Environmental Permit Approved (LA 27 East Side)	0 days	Fri 9/15/06	Fri 9/15/06		◆	Environmental Permit Approved (LA 27 East Side)		
111	Environmental Permit Approval (LA 27 West Side)	0 days	Fri 9/15/06	Fri 9/15/06		◆	Environmental Permit Approval (LA 27 West Side)		
97	Project Approval to Go to Construction (LA 27 East Side)	14 days	Mon 9/18/06	Thu 10/5/06		▣	Project Approval to Go to Construction (LA 27 East Side)		
112	Final Design (LA 27 West Side)	30 days	Mon 9/18/06	Fri 10/27/06		▣	Final Design (LA 27 West Side)		
98	Advertise/Bid Construction (LA 27 East Side)	30 days	Fri 10/6/06	Thu 11/16/06		▣	Advertise/Bid Construction (LA 27 East Side)		
113	Advertise/Bid Construction Contract (LA 27 West Side)	30 days	Mon 10/30/06	Fri 12/8/06		▣	Advertise/Bid Construction Contract (LA 27 West Side)		
99	Award/NTP Construction Contract (LA 27 East Side)	30 days	Fri 11/17/06	Thu 12/28/06		▣	Award/NTP Construction Contract (LA 27 East Side)		
114	Award/NTP Construction Contract (LA 27 West Side)	30 days	Mon 12/11/06	Fri 1/19/07		▣	Award/NTP Construction Contract (LA 27 West Side)		
100	Construct Improvements (LA 27 East Side)	250 days	Fri 12/29/06	Thu 12/13/07		▣	Construct Improvements (LA 27 East Side)		
115	Construct Improvements (LA 27 West Side)	250 days	Mon 1/22/07	Fri 1/4/08		▣	Construct Improvements (LA 27 West Side)		
	Water District Facilities Repairs	240 days	Mon 5/1/06	Fri 3/30/07	◆				
149	Approve/Fund Water Distribution/Treatment System Project	0 days	Mon 5/1/06	Mon 5/1/06	◆		Approve/Fund Water Distribution/Treatment System Project		
150	Determine Insurance/Public Assistance and Other Funding Sources	20 days	Mon 5/1/06	Fri 5/26/06	▣		Determine Insurance/Public Assistance and Other Funding Sources		
151	Solicit/Award Design Consultant	20 days	Mon 5/29/06	Fri 6/23/06	▣		Solicit/Award Design Consultant		
152	Develop Design/Plans/Specifications	40 days	Mon 6/26/06	Fri 8/18/06	▣		Develop Design/Plans/Specifications		
153	Advertise/Bid Construction Contract	20 days	Mon 8/21/06	Fri 9/15/06	▣		Advertise/Bid Construction Contract		
154	Award/NTP Construction Contract	20 days	Mon 9/18/06	Fri 10/13/06	▣		Award/NTP Construction Contract		
155	Construct Water Distribution/Treatment System Project	120 days	Mon 10/16/06	Fri 3/30/07	▣		Construct Water Distribution/Treatment System Project		

Project: CameSRT
Date: Mon 3/20/06

Task

Progress

Split

Summary


Project Summary

External Tasks

External Milestone

Deadline

Page 9

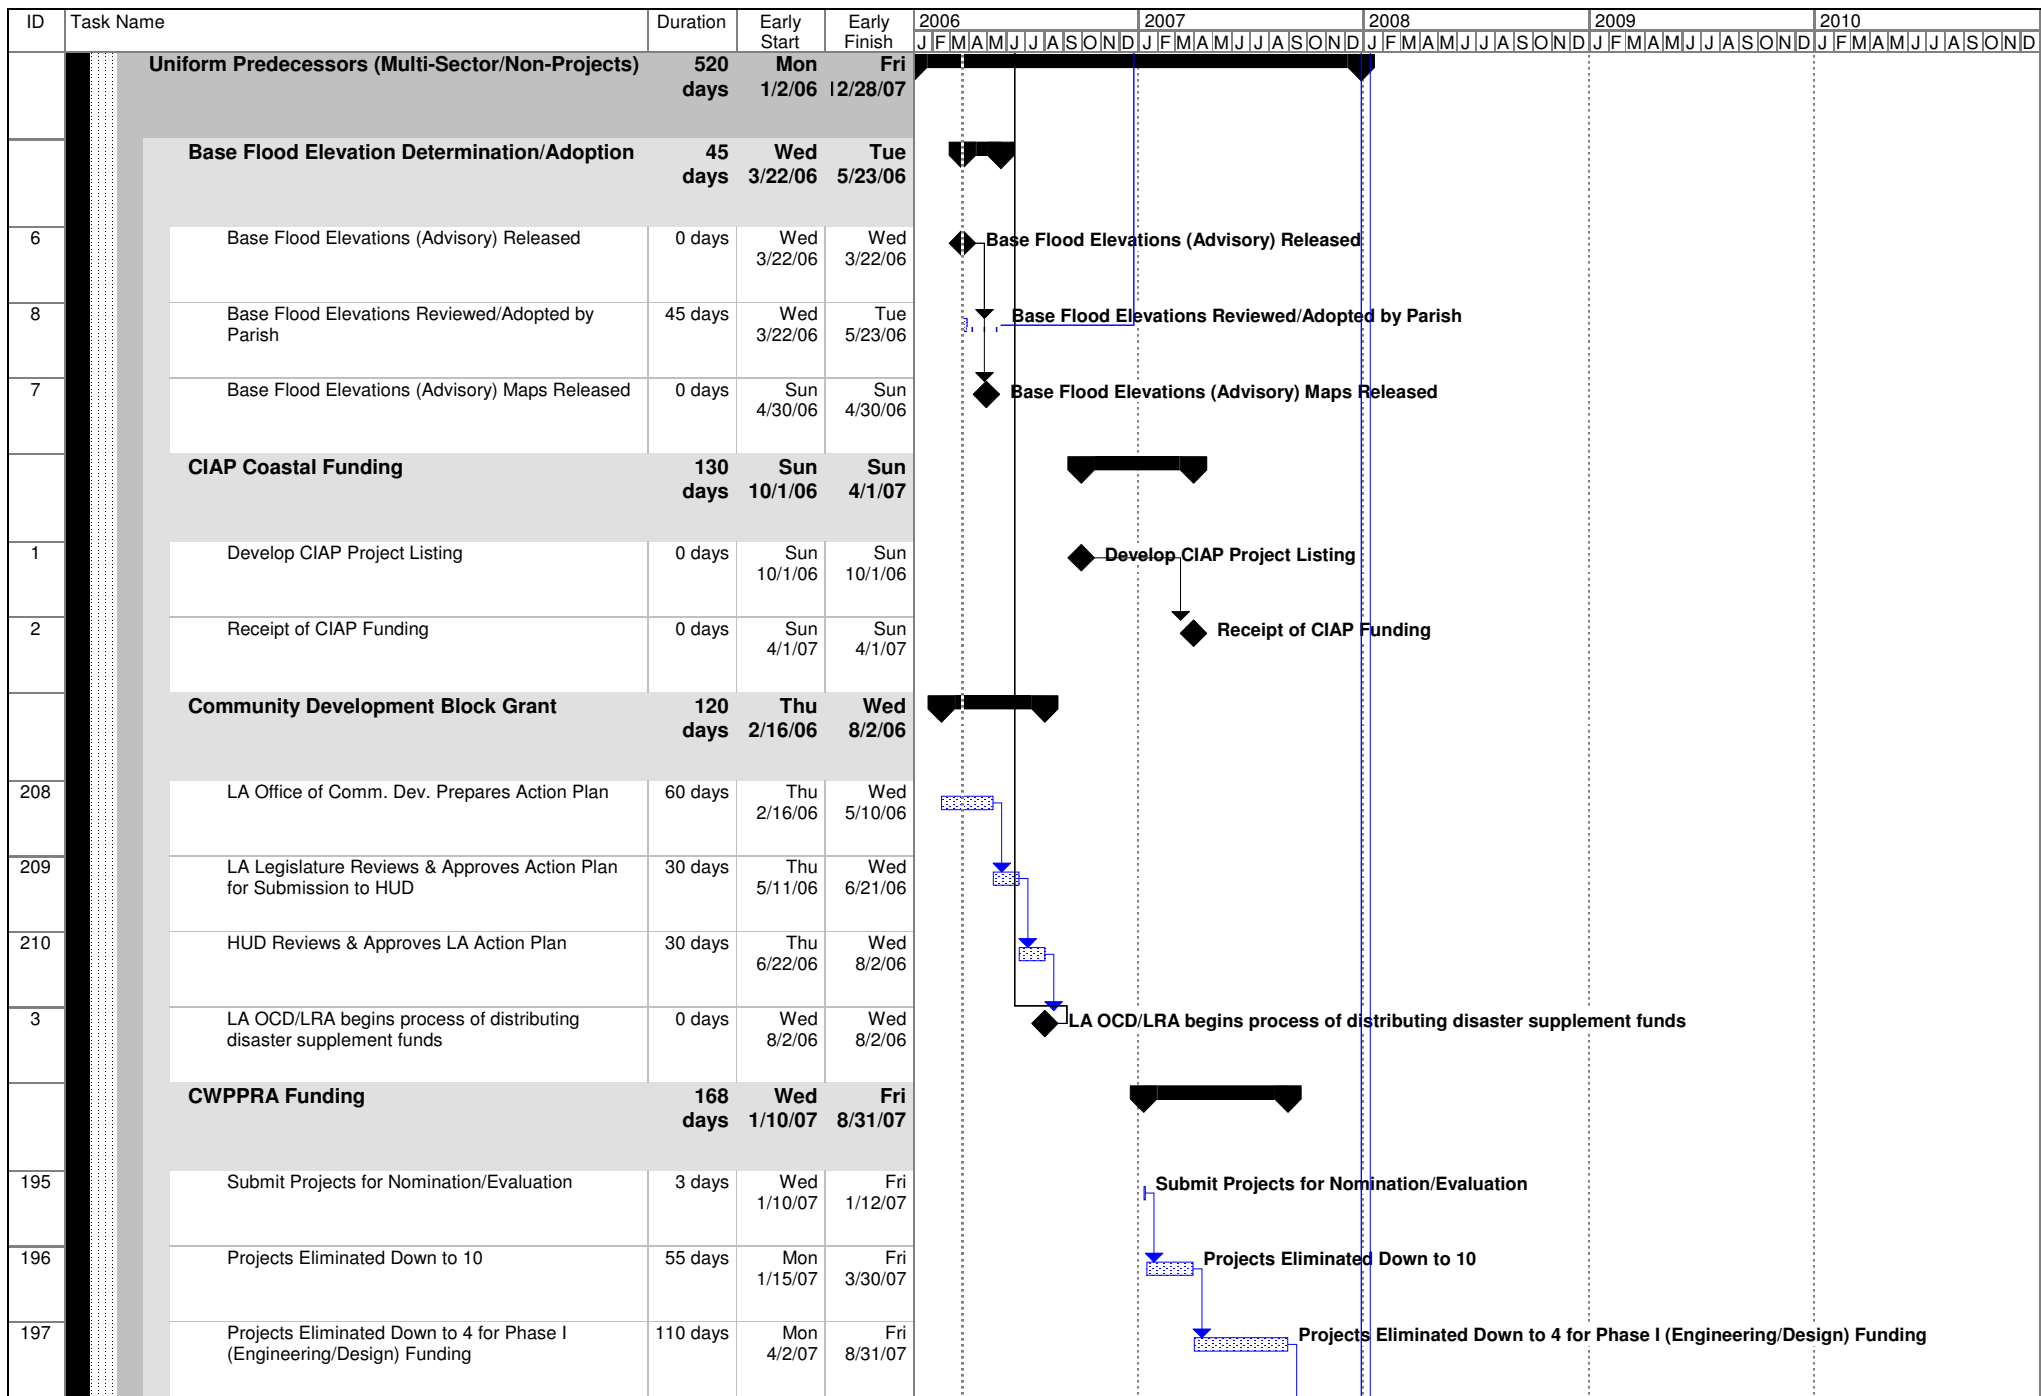

ID	Task Name	Duration	Early Start	Early Finish	2006	2007	2008	2009	2010																															
					J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
198	Phase I CWPPRA Funding Authorized	0 days	Fri 8/31/07	Fri 8/31/07	Phase I CWPPRA Funding Authorized																																			
	Dredged Material Management Plan (USACE)	500 days	Mon 1/16/06	Fri 12/14/07																																				
213	Dredged Material Management Plan	500 days	Mon 1/16/06	Fri 12/14/07																																				
	Hazard Mitigation Plan	67 days	Thu 2/16/06	Fri 5/19/06																																				
4	Parish Adoption & Submission of Documentation to State/FEMA	60 days	Thu 2/16/06	Wed 5/10/06																																				
5	Formal Haz Mitigation Plan Approval from FEMA	7 days	Thu 5/11/06	Fri 5/19/06																																				
	LA Coastal Protection & Restoration Study (USACE)	520 days	Mon 1/2/06	Fri 12/28/07																																				
211	Preliminary Design Report	120 days	Mon 1/2/06	Fri 6/16/06																																				
212	Final Design Report	400 days	Mon 6/19/06	Fri 12/28/07																																				
