


ID	Task Name	Duration	Early Start	Early Finish	2006		2007		2008		2009		2010				
					J	F	J	A	J	A	J	A	J	A	J	A	
<b>Region 5 - Orleans AFO</b>					<b>3302</b>	<b>Mon</b>	<b>Tue</b>										
		<b>days</b>	<b>1/2/06</b>	<b>8/28/18</b>													
<b>Plaquemines Parish</b>					<b>3302</b>	<b>Mon</b>	<b>Tue</b>										
		<b>days</b>	<b>1/2/06</b>	<b>8/28/18</b>													
<b>Economic &amp; Workforce Development</b>					<b>728</b>	<b>Mon</b>	<b>Wed</b>										
		<b>days</b>	<b>3/20/06</b>	<b>12/31/08</b>													
<b>Comprehensive Master Plan</b>					<b>321</b>	<b>Wed</b>	<b>Wed</b>										
		<b>days</b>	<b>3/22/06</b>	<b>6/13/07</b>													
187	Approve/Fund Project	0 days	Thu 6/1/06	Thu 6/1/06	◆ Approve/Fund Project												
188	Establish Steering Committee, Solicit/Award Consultant Contract for Comprehensive	90 days	Thu 6/1/06	Wed 10/4/06	▨ Establish Steering Committee, Solicit/Award Consultant Contract for Comprehe												
189	Tie to CDBG Funding	0 days	Wed 8/2/06	Wed 8/2/06	◆ Tie to CDBG Funding												
190	Tie to BFE Maps	0 days	Wed 3/22/06	Wed 3/22/06	◆ Tie to BFE Maps												
191	Develop Master Plan	180 days	Thu 10/5/06	Wed 6/13/07	▨ Develop Master Plan												
<b>Create Econ Dev, Comm Dev &amp; Planning In Parish</b>					<b>232</b>	<b>Thu</b>	<b>Fri</b>										
		<b>days</b>	<b>6/1/06</b>	<b>4/20/07</b>													
207	Approve/Fund Project	0 days	Thu 6/1/06	Thu 6/1/06	◆ Approve/Fund Project												
208	Obtain CDBG Funding/Hire Personnel	67 days	Thu 8/3/06	Fri 11/3/06	▨ Obtain CDBG Funding/Hire Personnel												
209	Administer Economic/Community Development & Parish Planning	120 days	Mon 11/6/06	Fri 4/20/07	▨ Administer Economic/Community Development & Parish Planning												
210	Tie to CDBG Funding	0 days	Wed 8/2/06	Wed 8/2/06	◆ Tie to CDBG Funding												
<b>Develop AMAX Port Facility &amp; Industrial Park</b>					<b>648</b>	<b>Mon</b>	<b>Wed</b>										
		<b>days</b>	<b>3/20/06</b>	<b>9/10/08</b>													
211	Approve/Fund Project	0 days	Mon 3/20/06	Mon 3/20/06	◆ Approve/Fund Project												
212	Site Being Cleaned	30 days	Mon 3/20/06	Fri 4/28/06	▨ Site Being Cleaned												
213	Negotiate Parish Purchase of Site	40 days	Thu 6/8/06	Wed 8/2/06	▨ Negotiate Parish Purchase of Site												
214	Tie to CDBG Funding	0 days	Wed 8/2/06	Wed 8/2/06	◆ Tie to CDBG Funding												
215	Parish Procure Site	50 days	Thu 8/3/06	Wed 10/11/06	▨ Parish Procure Site												
216	Develop AMAX Port Facility & Industrial Park	500 days	Thu 10/12/06	Wed 9/10/08	▨ Develop AMAX Port Facility & Industrial Park												
<b>Develop Oyster Hatchery &amp; Aquaculture Farming</b>					<b>160</b>	<b>Wed</b>	<b>Wed</b>										
		<b>days</b>	<b>8/2/06</b>	<b>3/14/07</b>													
37	Approve CDBG Funding	0 days	Wed 8/2/06	Wed 8/2/06	◆ Approve CDBG Funding												
38	Acquire/Lease Land in Buras	20 days	Thu 8/3/06	Wed 8/30/06	▨ Acquire/Lease Land in Buras												

Project: PLAQSR Date: Mon 3/20/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	





ID	Task Name	Duration	Early Start	Early Finish	2006					2007					2008					2009					2010																								
					J	F	A	J	J	A	S	O	N	D	J	F	A	J	J	A	S	O	N	D	J	F	A	J	J	A	S	O	N	D	J	F	A	J	J	A	S	O	N	D	J	F	A	J	J
196	Develop Budget to Become Self-Funding	490 days	Tue 10/31/06	Mon 9/15/08																																													
197	Identify Curriculum	60 days	Tue 3/21/06	Mon 6/12/06																																													
198	Accreditation	20 days	Tue 6/13/06	Mon 7/10/06																																													
199	Hire Staff	60 days	Tue 10/31/06	Mon 1/22/07																																													
200	Begin Operations	0 days	Mon 3/19/07	Mon 3/19/07																																													
201	Locate Facility	60 days	Tue 3/21/06	Mon 6/12/06																																													
202	Procure Equipment & Furnishings	200 days	Tue 6/13/06	Mon 3/19/07																																													
203	Market Programs	180 days	Tue 6/13/06	Mon 2/19/07																																													
<b>Education</b>			<b>240 days</b>	<b>Thu 6/1/06</b>	<b>Wed 5/2/07</b>																																												
<b>Plaquemines Parish Cyber Library &amp; Mobile Computer Lab</b>			<b>240 days</b>	<b>Thu 6/1/06</b>	<b>Wed 5/2/07</b>																																												
204	Approve/Fund Project	0 days	Thu 6/1/06	Thu 6/1/06																																													
205	Identify/Obtain Funds	120 days	Thu 6/1/06	Wed 11/15/06																																													
206	Order/Receive Mobile Library Vehicle	120 days	Thu 11/16/06	Wed 5/2/07																																													
<b>Flood Protection &amp; Coastal Restoration</b>			<b>3255 days</b>	<b>Wed 3/8/06</b>	<b>Tue 8/28/18</b>																																												
<b>Beneficial Use of Dredged Material</b>			<b>727 days</b>	<b>Fri 9/1/06</b>	<b>Mon 6/15/09</b>																																												
144	Approve/Fund Project	0 days	Fri 9/1/06	Fri 9/1/06																																													
145	Change Dredge Spoil Policy to Allow Placement of Material in Select Marshes	567 days	Fri 9/1/06	Mon 11/3/08																																													
146	Dredge Baptiste Colletta Channel	160 days	Tue 11/4/08	Mon 6/15/09																																													
<b>Coastal Parish Slurry Pipeline</b>			<b>830 days</b>	<b>Mon 5/1/06</b>	<b>Fri 7/3/09</b>																																												
331	Approve/Fund	0 days	Mon 5/1/06	Mon 5/1/06																																													
332	Perform Environmental Assessment/Permit Approval	120 days	Mon 5/1/06	Fri 10/13/06																																													
333	Phase I Design Trunk Line	120 days	Mon 5/1/06	Fri 10/13/06																																													
334	Phase I Contract/Award/Install Trunk Pipeline	250 days	Mon 10/16/06	Fri 9/28/07																																													
335	Phase II Establish Facilities for Marsh and Ridge Restoration	510 days	Mon 7/9/07	Fri 6/19/09																																													









ID	Task Name	Duration	Early Start	Early Finish	2006				2007				2008				2009				2010											
					J	F	A	M	J	J	A	S	O	N	D	J	F	A	M	J	J	J	A	S	O	N	D	J	F	A	M	J
53	Approve/Fund	0 days	Mon 5/1/06	Mon 5/1/06	◆ Approve/Fund																											
54	Perform Environmental Assessment	60 days	Mon 5/1/06	Fri 7/21/06	▨ Perform Environmental Assessment																											
55	Perform Environmental Cleanup	40 days	Mon 7/24/06	Fri 9/15/06	▨ Perform Environmental Cleanup																											
56	Obtain Political and Funding Support	120 days	Mon 9/18/06	Fri 3/2/07	▨ Obtain Political and Funding Support																											
57	Site Design and Master Plan	120 days	Mon 3/5/07	Fri 8/17/07	▨ Site Design and Master Plan																											
58	Obtain Permits	40 days	Mon 8/20/07	Fri 10/12/07	▨ Obtain Permits																											
59	Construction	180 days	Mon 10/15/07	Fri 6/20/08	▨ Construction																											
<b>Develop Subsidized Housing for Disabled Persons</b>		<b>1209 days</b>	<b>Thu 6/1/06</b>	<b>Tue 1/18/11</b>	▬																											
177	Approve/Fund Project	0 days	Thu 6/1/06	Thu 6/1/06	◆ Approve/Fund Project																											
178	Develop/Submit/Approval HUD Application for Disabled Persons Housing Subsidy	459 days	Thu 6/1/06	Tue 3/4/08	▨ Develop/Submit/Approval HUD Application for Disabl																											
179	Tie to Sewer Plant Capacity Expansion	0 days	Thu 6/1/06	Thu 6/1/06	◆ Tie to Sewer Plant Capacity Expansion																											
180	Tie to BFE Maps	0 days	Wed 8/2/06	Wed 8/2/06	◆ Tie to BFE Maps																											
181	Develop Subsidized Housing for Disabled Persons	750 days	Wed 3/5/08	Tue 1/18/11	▨																											
<b>Human Services</b>		<b>1058 days</b>	<b>Mon 5/1/06</b>	<b>Wed 5/19/10</b>	▬																											
<b>Acquisition &amp; Development of Parish State Park</b>		<b>990 days</b>	<b>Wed 8/2/06</b>	<b>Wed 5/19/10</b>	▬																											
263	Approve/Fund Project	0 days	Wed 8/2/06	Wed 8/2/06	◆ Approve/Fund Project																											
264	Tie to CDBG	0 days	Wed 8/2/06	Wed 8/2/06	◆ Tie to CDBG																											
265	Recruit State Legislator to Sponsor Park	60 days	Thu 8/3/06	Wed 10/25/06	▨ Recruit State Legislator to Sponsor Park																											
266	State of LA Performs Suitability Study	120 days	Thu 10/26/06	Wed 4/11/07	▨ State of LA Performs Suitability Study																											
267	State of LA Office of State Parks Hires Consultant to Perform Feasibility Study	40 days	Thu 4/12/07	Wed 6/6/07	▨ State of LA Office of State Parks Hires Consultant to Perform Feasi																											
268	Feasibility Study Performed	80 days	Thu 6/7/07	Wed 9/26/07	▨ Feasibility Study Performed																											
269	LA Office of State Parks Submits Capital Outlay Request	40 days	Thu 9/27/07	Wed 11/21/07	▨ LA Office of State Parks Submits Capital Outlay Request																											
270	Tie to Cleanup of Freeport-McMoran Site	0 days	Fri 4/27/07	Fri 4/27/07	◆ Tie to Cleanup of Freeport-McMoran Site																											
271	State of LA Contracts for a Master Plan Consultant	40 days	Thu 11/22/07	Wed 1/16/08	▨ State of LA Contracts for a Master Plan Consultant																											


Project: PLAQSR Date: Mon 3/20/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ID	Task Name	Duration	Early Start	Early Finish	2006			2007			2008			2009			2010												
					J	F	A	J	J	A	S	O	N	D	J	F	A	J	J	A	S	O	N	D	J	F	A	J	J
272	Develop Master Plan	180 days	Thu 1/17/08	Wed 9/24/08																									
273	Develop Construction Documents	250 days	Thu 9/25/08	Wed 9/9/09																									
274	Bid/Award/Construct Park	180 days	Thu 9/10/09	Wed 5/19/10																									
<b>Relocation of the Stadium at Fort Jackson</b>			<b>460 days</b>	<b>Mon 5/1/06</b>	<b>Fri 2/1/08</b>																								
275	Approve/Fund Project	0 days	Mon 5/1/06	Mon 5/1/06																									
276	Acquire New Stadium Site	120 days	Mon 5/1/06	Fri 10/13/06																									
277	Solicit Design Consultant	20 days	Mon 10/16/06	Fri 11/10/06																									
278	Award/Develop Design	60 days	Mon 11/13/06	Fri 2/2/07																									
279	Parish Council Approve Stadium Design	40 days	Mon 2/5/07	Fri 3/30/07																									
280	Advertise/Bid Stadium Construction	20 days	Mon 4/2/07	Fri 4/27/07																									
281	Award/NTP Stadium Construction Contract	20 days	Mon 4/30/07	Fri 5/25/07																									
282	Construct Stadium	180 days	Mon 5/28/07	Fri 2/1/08																									
283	Demo Existing Stadium at Jackson Site	40 days	Mon 5/1/06	Fri 6/23/06																									
<b>Public Health &amp; Healthcare</b>			<b>475 days</b>	<b>Wed 8/2/06</b>	<b>Wed 5/28/08</b>																								
<b>Plaquemines Medical Center Redevelopment &amp; Expansion</b>			<b>475 days</b>	<b>Wed 8/2/06</b>	<b>Wed 5/28/08</b>																								
249	Approve/Fund Project	0 days	Wed 8/2/06	Wed 8/2/06																									
250	Solicit/Award Consulting Contract to Evaluate Parish Medical Needs	60 days	Thu 8/3/06	Wed 10/25/06																									
251	Evaluate/Forecast Parish Medical Needs/Center Alternatives	190 days	Thu 10/26/06	Wed 7/18/07																									
252	Present Medical Needs Assessment to Parish Board	5 days	Thu 7/19/07	Wed 7/25/07																									
253	Parish to Select Medical Center Alternate	20 days	Thu 7/26/07	Wed 8/22/07																									
254	Solicit/Award Facility Design Consultant	20 days	Thu 8/23/07	Wed 9/19/07																									
255	Design/Plans/Specs/Bid Package	60 days	Thu 9/20/07	Wed 12/12/07																									
256	Advertise/Bid Medical Center Construction	20 days	Thu 12/13/07	Wed 1/9/08																									
257	Award/NTP Medical Center Construction	20 days	Thu 1/10/08	Wed 2/6/08																									

Project: PLAQSR Date: Mon 3/20/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	




ID	Task Name	Duration	Early Start	Early Finish	2006				2007				2008				2009				2010															
					J	F	A		J	J	A	S	O	N	D		J	F	A		J	J	A	S	O	N	D		J	F	A		J	J	A	S
258	Construct Medical Center	80 days	Thu 2/7/08	Wed 5/28/08																																
259	Tie to CDBG	0 days	Wed 8/2/06	Wed 8/2/06																																
260	Staff Mobile Medical Vehicle	80 days	Thu 8/3/06	Wed 11/22/06																																
261	Procure Mobile Medical Vehicle	80 days	Thu 8/3/06	Wed 11/22/06																																
262	Operate Mobile Medical Vehicle	0 days	Wed 11/22/06	Wed 11/22/06																																
	<b>Public Safety</b>	<b>520 days</b>	<b>Thu 3/1/07</b>	<b>Wed 2/25/09</b>																																
	<b>Emergency Preparedness Operations Center (ICC)</b>	<b>265 days</b>	<b>Thu 3/1/07</b>	<b>Wed 3/5/08</b>																																
67	Approve/Fund East ICC	0 days	Thu 3/1/07	Thu 3/1/07																																
68	Conceptual Design East Center	40 days	Thu 3/1/07	Wed 4/25/07																																
69	Identify Site	5 days	Thu 4/26/07	Wed 5/2/07																																
70	Solicit/Award Design Consultant	20 days	Thu 5/3/07	Wed 5/30/07																																
71	Complete Design	40 days	Thu 5/31/07	Wed 7/25/07																																
72	Advertise/Bid Construction	20 days	Thu 7/26/07	Wed 8/22/07																																
73	Award/NTP Construction	20 days	Thu 8/23/07	Wed 9/19/07																																
74	Procure Equipment	40 days	Thu 7/26/07	Wed 9/19/07																																
75	Construct East ICC	120 days	Thu 9/20/07	Wed 3/5/08																																
76	Approve/Fund West ICC	0 days	Thu 3/1/07	Thu 3/1/07																																
77	Conceptual Design West Center	40 days	Thu 3/1/07	Wed 4/25/07																																
78	Identify Site	5 days	Thu 4/26/07	Wed 5/2/07																																
79	Solicit/Award Design Consultant	20 days	Thu 5/3/07	Wed 5/30/07																																
80	Complete Design	40 days	Thu 5/31/07	Wed 7/25/07																																
81	Advertise/Bid Construction	20 days	Thu 7/26/07	Wed 8/22/07																																
82	Award/NTP Construction	20 days	Thu 8/23/07	Wed 9/19/07																																
83	Procure Equipment	40 days	Thu 7/26/07	Wed 9/19/07																																
84	Construct West ICC	120 days	Thu 9/20/07	Wed 3/5/08																																

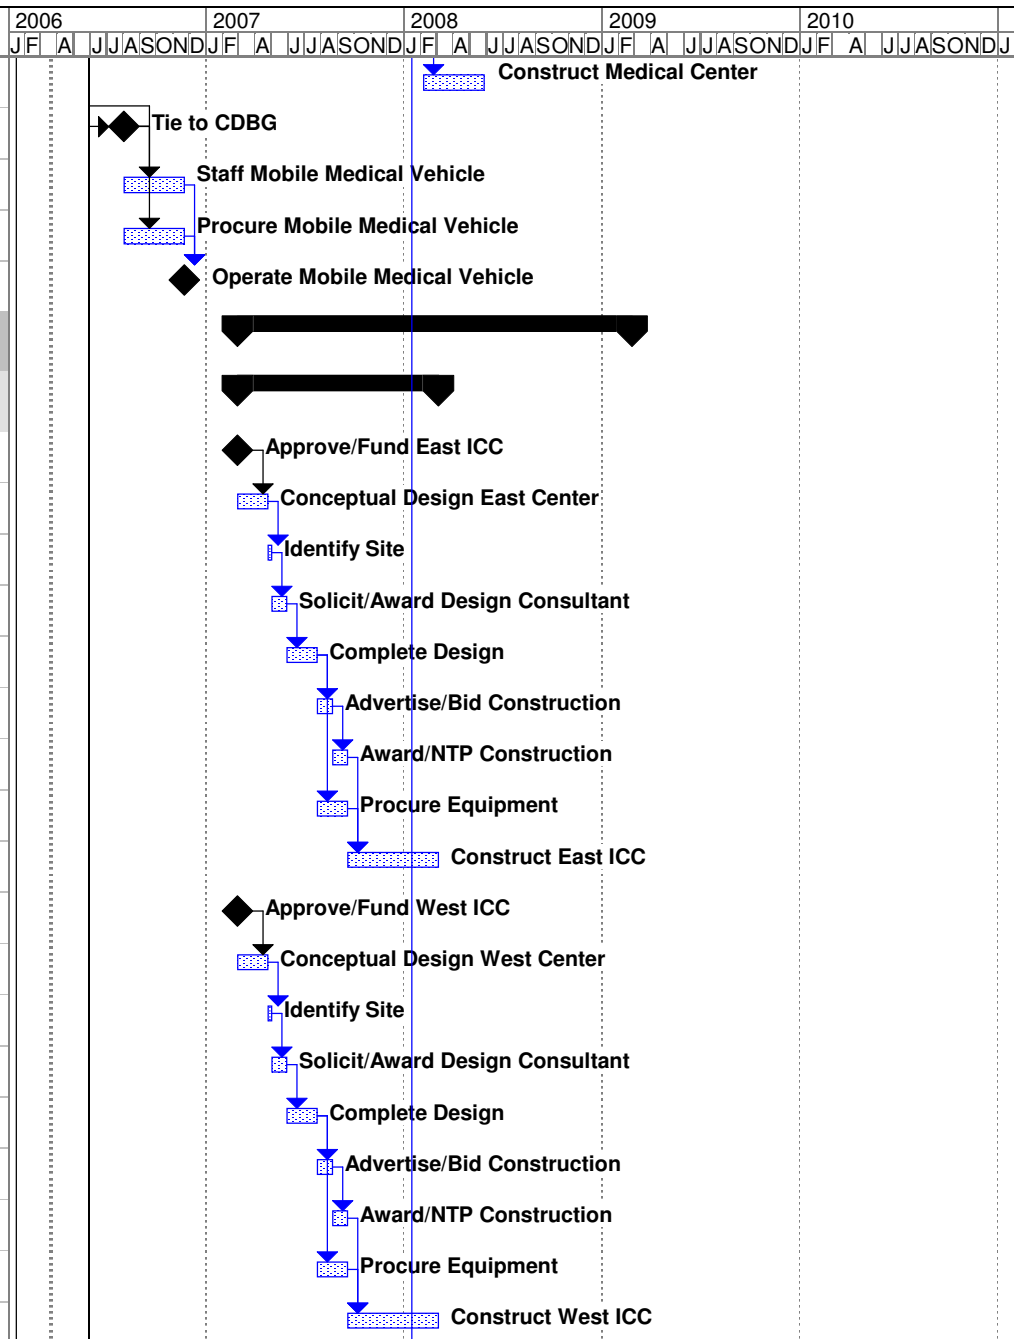

Project: PLAQSR Date: Mon 3/20/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	


ID	Task Name	Duration	Early Start	Early Finish	2006					2007					2008					2009					2010																								
					J	F	A	J	J	A	S	O	N	D	J	F	A	J	J	A	S	O	N	D	J	F	A	J	J	A	S	O	N	D	J	F	A	J	J	A	S	O	N	D	J	F	A	J	J
<b>Sheriff's Office Restoration/Consolidation</b>		<b>520 days</b>	<b>Thu</b>	<b>Wed</b>																																													
			<b>3/1/07</b>	<b>2/25/09</b>																																													
85	Approve/Fund North Plaquemines Law Enforcement Complex	0 days	Thu 3/1/07	Thu 3/1/07																																													
86	Conceptual Design North Plaquemines Law Enforcement Complex	40 days	Thu 3/1/07	Wed 4/25/07																																													
87	Identify Site	40 days	Thu 4/26/07	Wed 6/20/07																																													
88	Solicit/Award Design Consultant	20 days	Thu 6/21/07	Wed 7/18/07																																													
89	Complete Design	120 days	Thu 7/19/07	Wed 1/2/08																																													
90	Advertise/Bid Construction	40 days	Thu 1/3/08	Wed 2/27/08																																													
91	Award/NTP Construction	20 days	Thu 2/28/08	Wed 3/26/08																																													
92	Procure Equipment	80 days	Thu 1/3/08	Wed 4/23/08																																													
93	Construct North Plaquemines Law Enforcement Complex	220 days	Thu 4/24/08	Wed 2/25/09																																													
94	Approve/Fund South Plaquemines Law Enforcement Complex	0 days	Thu 3/1/07	Thu 3/1/07																																													
95	Conceptual Design South Plaquemines Law Enforcement Complex	40 days	Thu 3/1/07	Wed 4/25/07																																													
96	Identify Site	40 days	Thu 4/26/07	Wed 6/20/07																																													
97	Solicit/Award Design Consultant	20 days	Thu 6/21/07	Wed 7/18/07																																													
98	Complete Design	120 days	Thu 7/19/07	Wed 1/2/08																																													
99	Advertise/Bid Construction	40 days	Thu 1/3/08	Wed 2/27/08																																													
100	Award/NTP Construction	20 days	Thu 2/28/08	Wed 3/26/08																																													
101	Procure Equipment	80 days	Thu 1/3/08	Wed 4/23/08																																													
102	Construct South Plaquemines Law Enforcement Complex	220 days	Thu 4/24/08	Wed 2/25/09																																													
103	Approve/Fund East Bank Plaquemines Law Enforcement Complex	0 days	Thu 3/1/07	Thu 3/1/07																																													
104	Conceptual Design East Bank Plaquemines Law Enforcement Complex	40 days	Thu 3/1/07	Wed 4/25/07																																													
105	Identify Site	40 days	Thu 4/26/07	Wed 6/20/07																																													
106	Solicit/Award Design Consultant	20 days	Thu 6/21/07	Wed 7/18/07																																													
107	Complete Design	120 days	Thu 7/19/07	Wed 1/2/08																																													
108	Advertise/Bid Construction	40 days	Thu 1/3/08	Wed 2/27/08																																													

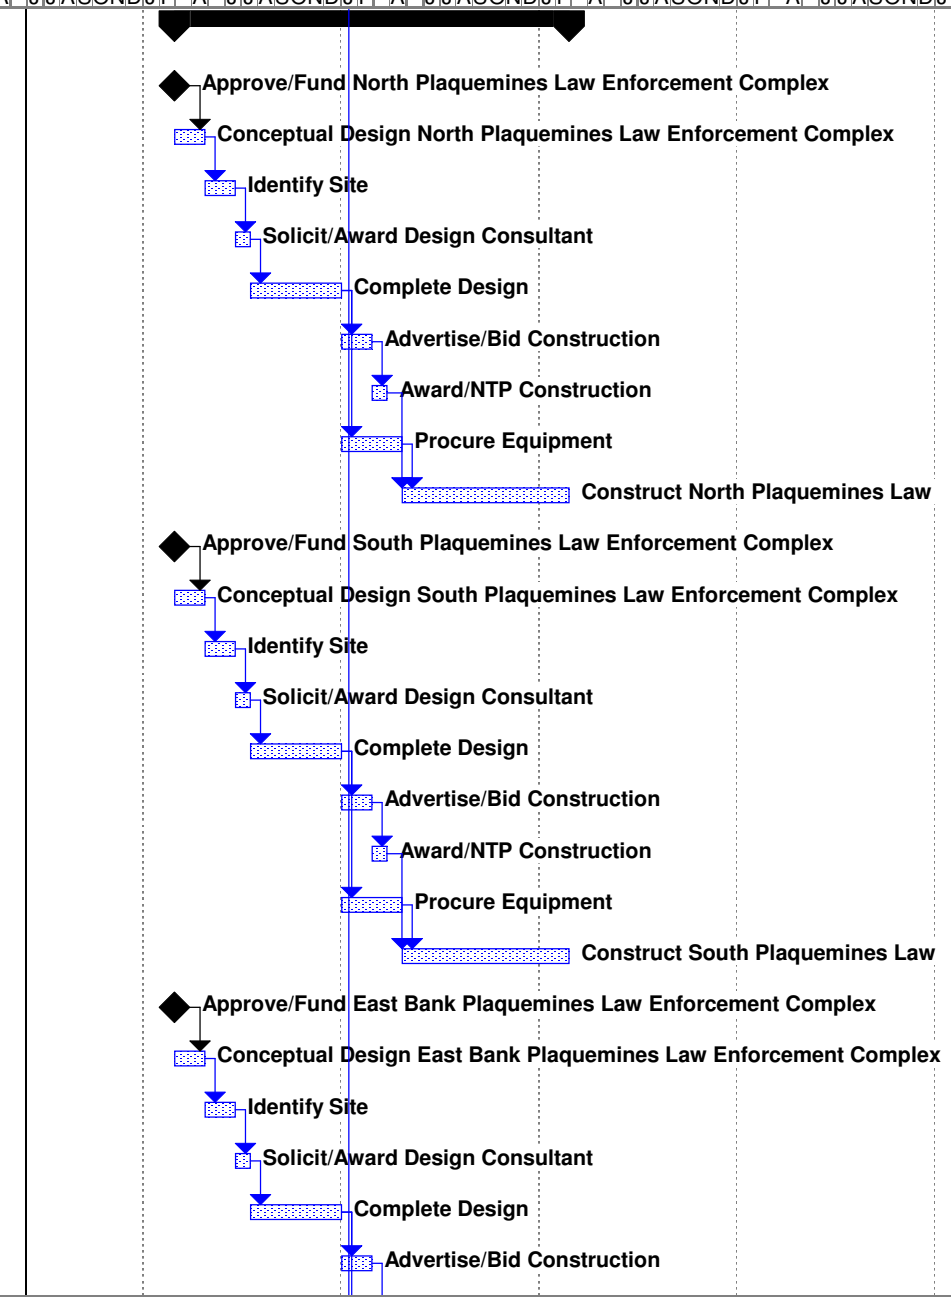

Project: PLAQSR Date: Mon 3/20/0	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	



ID	Task Name	Duration	Early Start	Early Finish	2006				2007				2008				2009				2010															
					J	F	A		J	J	A	S	O	N	D		J	F	A		J	J	A	S	O	N	D		J	F	A		J	J	A	S
286	Solicit Design Consultant	20 days	Thu 8/3/06	Wed 8/30/06																																
287	Award/Develop Road and Bridge Design	500 days	Thu 8/31/06	Wed 7/30/08																																
288	Advertise/Bid Road and Bridge Construction	20 days	Thu 7/31/08	Wed 8/27/08																																
289	Award/NTP Road and Bridge Construction Contract	20 days	Thu 8/28/08	Wed 9/24/08																																
290	Construct Road and Bridge	600 days	Thu 9/25/08	Wed 1/12/11																																
	<b>Water &amp; Waste Water Repair, Expansion &amp; Maintenance</b>	<b>1300 days</b>	<b>Mon 5/1/06</b>	<b>Fri 4/22/11</b>																																
112	Approve/Fund Phase I Sewage Treatment Plant	0 days	Mon 5/1/06	Mon 5/1/06																																
113	Conceptual Design Phase I/II Sewage Treatment Plant & GIS	120 days	Mon 5/1/06	Fri 10/13/06																																
114	Identify Site	40 days	Mon 10/16/06	Fri 12/8/06																																
115	Solicit/Award Design Consultant	40 days	Mon 12/11/06	Fri 2/2/07																																
116	Complete Design	240 days	Mon 2/5/07	Fri 1/4/08																																
117	Advertise/Bid Construction	40 days	Mon 1/7/08	Fri 2/29/08																																
118	Award/NTP Construction	20 days	Mon 3/3/08	Fri 3/28/08																																
119	Procure Equipment	120 days	Mon 1/7/08	Fri 6/20/08																																
120	Construct East Belle Chasse Sewage Treatment Plant	740 days	Mon 6/23/08	Fri 4/22/11																																
121	Construct Boothville Sewage Treatment Plant	500 days	Mon 6/23/08	Fri 5/21/10																																
122	Construct Belle Chasse Sewerage	740 days	Mon 6/23/08	Fri 4/22/11																																
123	Construct Engineer's Road Sewerage	480 days	Mon 6/23/08	Fri 4/23/10																																
124	Construct Cedar Grove to La Reussite Sewerage	740 days	Mon 6/23/08	Fri 4/22/11																																
125	Construct West Point-a-la-Hache/Pointe Celeste Sewerage	480 days	Mon 6/23/08	Fri 4/23/10																																
126	Construct Happy Jack Marina Sewerage	480 days	Mon 6/23/08	Fri 4/23/10																																
127	Construct Nairn to Venice Gaps	480 days	Mon 6/23/08	Fri 4/23/10																																
128	Construct Braithwaite to White Ditch Sewerage	480 days	Mon 6/23/08	Fri 4/23/10																																
129	Construct Phoenix to Bohemia Sewerage	80 days	Mon 6/23/08	Fri 10/10/08																																
	<b>Woodland Highway (LA 406) Widening</b>	<b>760 days</b>	<b>Wed 8/2/06</b>	<b>Wed 7/1/09</b>																																

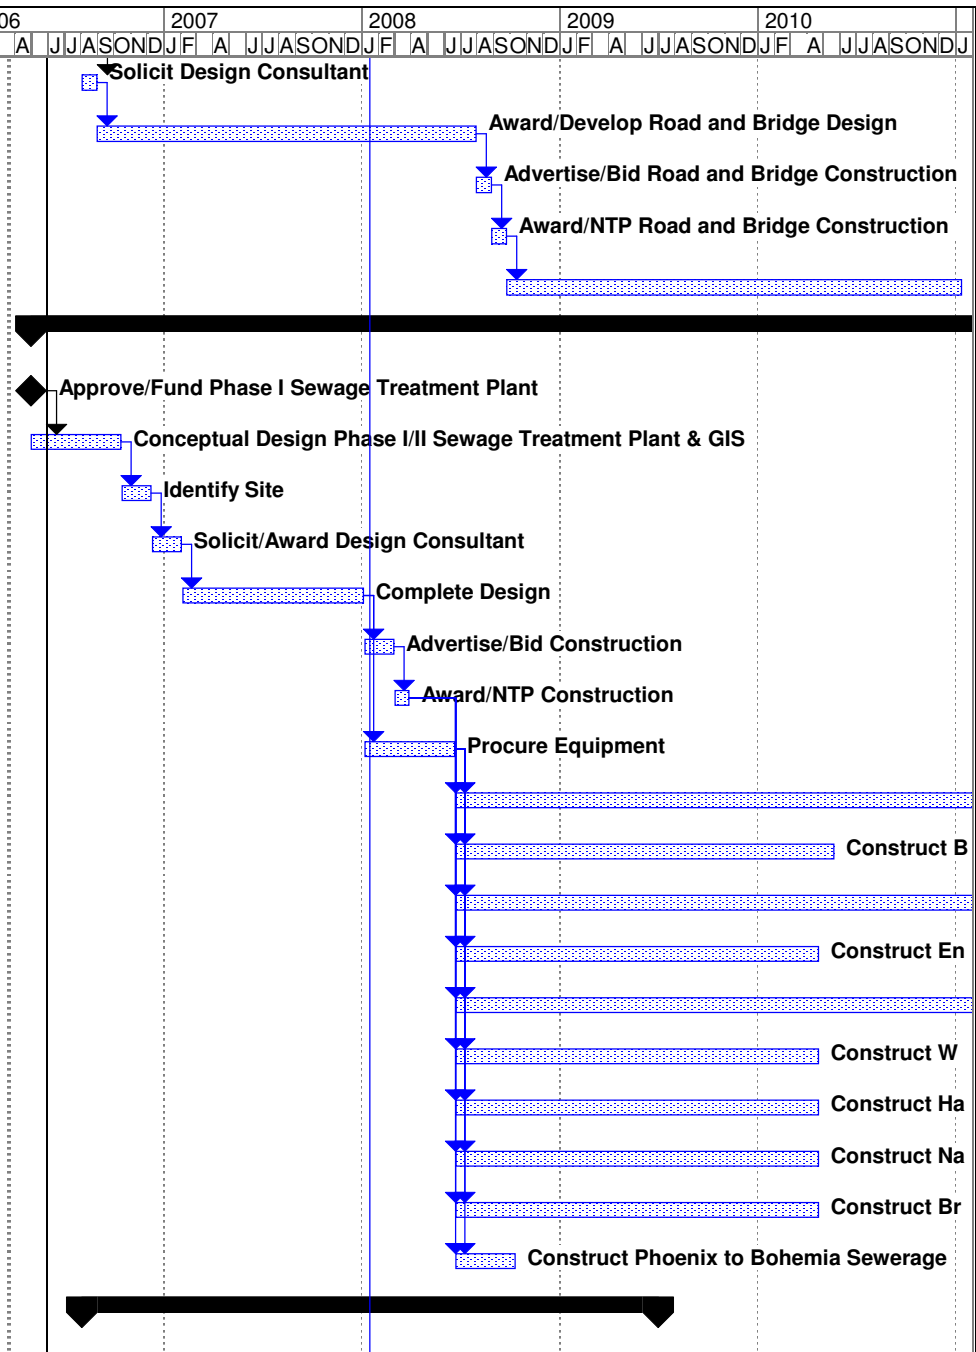

Project: PLAQSR Date: Mon 3/20/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ID	Task Name	Duration	Early Start	Early Finish	2006				2007				2008				2009				2010											
					J	F	A		J	J	A	S	O	N	D	J	F	A		J	J	A	S	O	N	D	J	F	A		J	J
306	Approve/Fund Project	0 days	Wed 8/2/06	Wed 8/2/06				◆	<b>Approve/Fund Project</b>																							
307	Tie to CDBG	0 days	Wed 8/2/06	Wed 8/2/06				◆	<b>Tie to CDBG</b>																							
308	Solicit Woodland Highway Design Consultant	20 days	Thu 8/3/06	Wed 8/30/06				■	<b>Solicit Woodland Highway Design Consultant</b>																							
309	Award/Develop Woodland Highway Design	200 days	Thu 8/31/06	Wed 6/6/07				■	<b>Award/Develop Woodland Highway Design</b>																							
310	Advertise/Bid Signal Construction	20 days	Thu 6/7/07	Wed 7/4/07				■	<b>Advertise/Bid Signal Construction</b>																							
311	Award/NTP Woodland Construction Contract	20 days	Thu 7/5/07	Wed 8/1/07				■	<b>Award/NTP Woodland Construction Contract</b>																							
312	Construct Woodland Highway Widening	500 days	Thu 8/2/07	Wed 7/1/09				■	<b>Construct Woodland Highway Widening</b>																							
	<b>Uniform Predecessors (Multi-Sector/Non-Projects)</b>	<b>520 days</b>	<b>Mon 1/2/06</b>	<b>Fri 12/28/07</b>	<b>Uniform Predecessors</b>																											
	<b>Base Flood Elevation Determination/Adoption</b>	<b>28 days</b>	<b>Wed 3/22/06</b>	<b>Sun 4/30/06</b>	<b>Base Flood Elevation Determination/Adoption</b>																											
1	Base Flood Elevations Adopted by Parish Council	10 days	Wed 3/22/06	Tue 4/4/06				◆	<b>Base Flood Elevations Adopted by Parish Council</b>																							
2	Base Flood Elevation (Advisory) Maps Released	0 days	Sun 4/30/06	Sun 4/30/06				◆	<b>Base Flood Elevation (Advisory) Maps Released</b>																							
5	Base Flood Elevations (Advisory) Released	0 days	Wed 3/22/06	Wed 3/22/06				◆	<b>Base Flood Elevations (Advisory) Released</b>																							
	<b>CIAP Funding for Coastal Projects</b>	<b>130 days</b>	<b>Sun 10/1/06</b>	<b>Sun 4/1/07</b>	<b>CIAP Funding for Coastal Projects</b>																											
325	Develop CIAP Project Listing	0 days	Sun 10/1/06	Sun 10/1/06				◆	<b>Develop CIAP Project Listing</b>																							
326	Receipt of CIAP Funding	0 days	Sun 4/1/07	Sun 4/1/07				◆	<b>Receipt of CIAP Funding</b>																							
	<b>Community Development Block Grants</b>	<b>120 days</b>	<b>Thu 2/16/06</b>	<b>Wed 8/2/06</b>	<b>Community Development Block Grants</b>																											
337	LA Office of Comm. Dev. Prepares Action Plan	60 days	Thu 2/16/06	Wed 5/10/06				■	<b>LA Office of Comm. Dev. Prepares Action Plan</b>																							
338	LA Legislature Reviews & Approves Action Plan for Submission to HUD	30 days	Thu 5/11/06	Wed 6/21/06				■	<b>LA Legislature Reviews &amp; Approves Action Plan for Submission to HUD</b>																							
341	HUD Reviews & Approves LA Action Plan	30 days	Thu 6/22/06	Wed 8/2/06				■	<b>HUD Reviews &amp; Approves LA Action Plan</b>																							
342	LA OCD/LRA begins process of distributing disaster supplement funds	0 days	Wed 8/2/06	Wed 8/2/06				◆	<b>LA OCD/LRA begins process of distributing disaster supplement funds</b>																							
	<b>CWPPRA Funding</b>	<b>168 days</b>	<b>Wed 1/10/07</b>	<b>Fri 8/31/07</b>	<b>CWPPRA Funding</b>																											
327	Submit Projects for Nomination/Evaluation	3 days	Wed 1/10/07	Fri 1/12/07				■	<b>Submit Projects for Nomination/Evaluation</b>																							
328	Projects Eliminated Down to 10	55 days	Mon 1/15/07	Fri 3/30/07				■	<b>Projects Eliminated Down to 10</b>																							
329	Projects Eliminated Down to 4 for Phase I (Engineering/Design) Funding	110 days	Mon 4/2/07	Fri 8/31/07				■	<b>Projects Eliminated Down to 4 for Phase I (Engineering/Design) Funding</b>																							

Project: PLAQSR Date: Mon 3/20/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ID	Task Name	Duration	Early Start	Early Finish	2006	2007	2008	2009	2010																														
					J	F	A	J	J	A	S	O	N	D	J	F	A	J	J	A	S	O	N	D	J	F	A	J	J	A	S	O	N	D	J	F	A		
330	Phase I CWPPRA Funding Authorized	0 days	Fri 8/31/07	Fri 8/31/07																																			
	<b>Hazard Mitigation Plan</b>	<b>67 days</b>	<b>Thu 2/16/06</b>	<b>Fri 5/19/06</b>																																			
3	Parish Adoption & Submission of Documentation to State/FEMA	60 days	Thu 2/16/06	Wed 5/10/06																																			
4	Formal Haz Mitigation Plan Approval from FEMA	7 days	Thu 5/11/06	Fri 5/19/06																																			
	<b>LA Coastal Protection &amp; Restoration Study (USACE)</b>	<b>520 days</b>	<b>Mon 1/2/06</b>	<b>Fri 12/28/07</b>																																			
343	Preliminary Design Report	120 days	Mon 1/2/06	Fri 6/16/06																																			
344	Final Design Report	400 days	Mon 6/19/06	Fri 12/28/07																																			
	<b>Task Force Guardian (USACE)</b>	<b>99 days</b>	<b>Mon 1/16/06</b>	<b>Thu 6/1/06</b>																																			
345	Repair Levees to Pre-Katrina Standards	99 days	Mon 1/16/06	Thu 6/1/06																																			



Project: PLAQSR Date: Mon 3/20/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	
