


ID	Task Name	Duration	Early Start	Early Finish	6	2007	2008	2009	2010
						M A M J J A S O N D	J F M A M J J A S O N D	J F M A M J J A S O N D	J F M A M J J A S O N D
	Region 5 - Orleans AFO	1712 days	Mon 1/2/06	Tue 7/24/12					
	St Bernard Parish	1712 days	Mon 1/2/06	Tue 7/24/12					
	Economic & Workforce Development	760 days	Mon 3/20/06	Fri 2/13/09					
	Festival Park Development	475 days	Tue 8/1/06	Mon 5/26/08					
188	Approve/Fund Project	0 days	Tue 8/1/06	Tue 8/1/06					
189	Initial Arrangements, Soliciting & Engaging	75 days	Tue 8/1/06	Mon 11/13/06					
190	Detailed Design & Reviews (Bids, Review, Contracting, NTP)	120 days	Tue 11/14/06	Mon 4/30/07					
191	Obtain Permits & Clearances (for Parish-Owned Val Reiss Pk.)	65 days	Tue 12/19/06	Mon 3/19/07					
192	Parish Considers & Establishes Staffing	60 days	Tue 9/18/07	Mon 12/10/07					
193	Indoor (Building) & Outdoor Construction of Festival Park	280 days	Tue 5/1/07	Mon 5/26/08					
	Ice House & Seafood/Farmers Market	570 days	Thu 6/1/06	Wed 8/6/08					
160	Approve/Fund Project	0 days	Thu 6/1/06	Thu 6/1/06					
161	Issue RFP, Review Proposals, Select & Contract with Designer	60 days	Thu 6/1/06	Wed 8/23/06					
162	Site Investigtn., Determtn. & Acquistn.	45 days	Thu 6/1/06	Wed 8/2/06					
163	Conceptual Design Underway/Completion	45 days	Thu 8/24/06	Wed 10/25/06					
164	Parish Reviews & Officially Accepts (Concpt.Design & Site)	15 days	Thu 10/26/06	Wed 11/15/06					
165	Detailed Design & Permitting	90 days	Thu 11/16/06	Wed 3/21/07					
166	Advertise & Receive Construction/Contractor Bids	30 days	Thu 3/22/07	Wed 5/2/07					
167	Review Bids/Documents, Contract for Construction & Issue NTP	30 days	Thu 5/3/07	Wed 6/13/07					
168	Water Treatm.Capac.Improv.Construction	0 days	Fri 11/23/07	Fri 11/23/07					
169	Waste-Water Treatm.Consolid.Construction Allows	0 days	Fri 12/21/07	Fri 12/21/07					
170	Seafood Market & Ice House Construction	300 days	Thu 6/14/07	Wed 8/6/08					
	Old Arabi Historic Neighborhood Revitalization	750 days	Mon 4/3/06	Fri 2/13/09					
1	Approve/Fund Project	0 days	Mon 4/3/06	Mon 4/3/06					

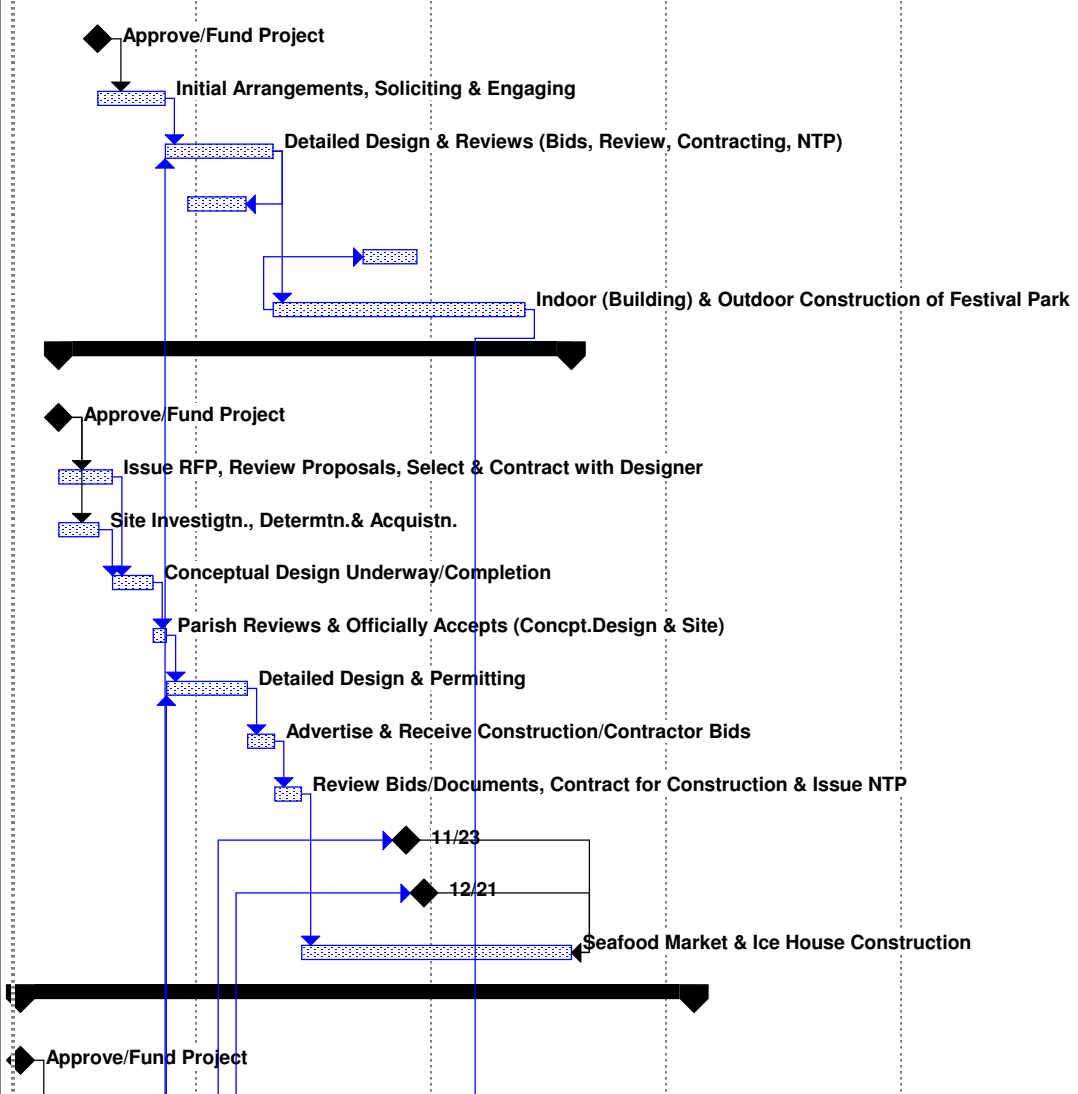

Project: STBESRT Date: Mon 3/20/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	


Page 1

ID	Task Name	Duration	Early Start	Early Finish	6	2007	2008	2009	2010
						M A M J J A S O N D	J F M A M J J A S O N D	J F M A M J J A S O N D	J F M A M J J A S O N D
2	Initial Arrangements, Soliciting & Engaging	60 days	Mon 4/3/06	Fri 6/23/06		Initial Arrangements, Soliciting & Engaging			
3	Land/Easement Investigation, Determination & Acquisition	200 days	Mon 5/15/06	Fri 2/16/07					
136	Industrial Access Route Design/Construction	420 days	Mon 6/26/06	Fri 2/1/08		Industrial Access Route Design/Construction			
137	Scenic River Overlook Design/Construction	240 days	Mon 10/30/06	Fri 9/28/07		Scenic River Overlook Design/Construction			
138	Public Square Development (at Pier & include LeBeau Plantation)	540 days	Mon 9/18/06	Fri 10/10/08		Public Square Development (at Pier & include LeBeau Plantation)			
139	Parking, Streetscape & Drainage Design/Construction	300 days	Mon 10/1/07	Fri 11/21/08		Parking, Streetscape & Drainage Design/Construction			
140	N.Peters Widening/Resurfacing Design/Construction	300 days	Mon 12/24/07	Fri 2/13/09		N.Peters Widening/Resurfacing Design/Construction			
141	Drainage at E.side of Center St. & Watermain Design/Construction	270 days	Mon 11/12/07	Fri 11/21/08		Drainage at E.side of Center St. & Watermain Design/Construction			
	Parish-Wide Wireless Internet Access	225 days	Mon 3/20/06	Fri 1/26/07		Parish-Wide Wireless Internet Access			
153	Demonstrate Program & Build Partnerships	40 days	Mon 3/20/06	Fri 5/12/06		Demonstrate Program & Build Partnerships			
154	Approve/Fund Project	0 days	Mon 5/1/06	Mon 5/1/06	◆	5/1			
155	Solicit, Select & Engage Vendor	45 days	Mon 4/24/06	Fri 6/23/06					
156	Conduct Field/Feasibility Study	50 days	Mon 6/26/06	Fri 9/1/06					
157	Policy, Fees, Assignms. are Determined/Approved & then Enforced	50 days	Mon 9/4/06	Fri 11/10/06					
158	Phase-1 Establish Hot-Spots at Specific Public Places	45 days	Mon 9/4/06	Fri 11/3/06					
159	Phase-2 Finish Wireless Access Parish-Wide	60 days	Mon 11/6/06	Fri 1/26/07					
	Small Business Services Center Creation	450 days	Mon 5/1/06	Fri 1/18/08		Small Business Services Center Creation			
143	Approve/Fund Project	0 days	Mon 5/1/06	Mon 5/1/06	◆	Approve/Fund Project			
145	Issue RFP, Review Proposals, Select & Contract with Designer	60 days	Mon 5/1/06	Fri 7/21/06		Issue RFP, Review Proposals, Select & Contract with Designer			
146	Site Investigation/Determination	45 days	Mon 5/1/06	Fri 6/30/06		Site Investigation/Determination			
147	Conceptual Design Underway/Completion	45 days	Mon 7/24/06	Fri 9/22/06		Conceptual Design Underway/Completion			
148	Parish Reviews & Officially Accepts (Concpt.Design & Site)	15 days	Mon 9/25/06	Fri 10/13/06		Parish Reviews & Officially Accepts (Concpt.Design & Site)			
149	Detailed Design Underway/Completion	60 days	Mon 10/16/06	Fri 1/5/07		Detailed Design Underway/Completion			
150	Advertise & Receive Construction/Contractor Bids	30 days	Mon 1/8/07	Fri 2/16/07		Advertise & Receive Construction/Contractor Bids			

Project: STBESRT Date: Mon 3/20/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	


ID	Task Name	Duration	Early Start	Early Finish	2007												2008												2009												2010																																																													
					M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D																																																				
151	Review Bids/Assoc.Documents, Contract for Construction & Issue NTP	30 days	Mon 2/19/07	Fri 3/30/07																																																																																																		
152	Sm.Bus.Serv.Center Construction Underway/Completion	210 days	Mon 4/2/07	Fri 1/18/08																																																																																																		
Town Center Development		560 days	Mon 4/3/06	Fri 5/23/08																																																																																																		
199	Approve/Fund Phase-1 of Project	0 days	Mon 4/3/06	Mon 4/3/06																																																																																																		
200	Issue RFP, Review Proposals, Select & Contract with Consultant	50 days	Mon 4/3/06	Fri 6/9/06																																																																																																		
201	Market & Urban Design Study (Phase-1, Plan & Site)	60 days	Mon 6/12/06	Fri 9/1/06																																																																																																		
202	Parish Reviews & Accepts (Plan & Site) & Additional Funding Confirmed	25 days	Mon 9/4/06	Fri 10/6/06																																																																																																		
203	Engagem., Design & Permit. (Ph.2 Infrastructure & Ph.3 Streetscape)	120 days	Mon 10/9/06	Fri 3/23/07																																																																																																		
204	Advertise & Receive Construction/Contractor Bids (Ph.2 & Ph.3)	25 days	Mon 3/26/07	Fri 4/27/07																																																																																																		
205	Review Bids/Documents, Contract for Construction & Issue NTP	30 days	Mon 4/30/07	Fri 6/8/07																																																																																																		
206	Water Treatm.Capac. Improv. Construction Allows Water Serv.	0 days	Fri 12/21/07	Fri 12/21/07																																																																																																		
207	Waste-Water Treatm.Consolid. Construction Allows San.Sewer Serv.	0 days	Fri 1/18/08	Fri 1/18/08																																																																																																		
208	Storm Water Sewer Upgrade Construction Allows Site Drainage	0 days	Wed 12/19/07	Wed 12/19/07																																																																																																		
209	Phase 2 & 3 Town Center Construction	250 days	Mon 6/11/07	Fri 5/23/08																																																																																																		
Education		510 days	Mon 8/21/06	Fri 8/1/08																																																																																																		
Chalmette H.S. Theater & Fine Arts Addition		510 days	Mon 8/21/06	Fri 8/1/08																																																																																																		
256	Approve/Fund Project	0 days	Mon 9/4/06	Mon 9/4/06																																																																																																		
257	Issue RFP, Review Proposals, Select & Contract with Designer	50 days	Mon 8/21/06	Fri 10/27/06																																																																																																		
258	Conceptual Design Underway/Completion	45 days	Mon 10/30/06	Fri 12/29/06																																																																																																		
259	School Board Reviews & Officially Accepts Conceptual Design	15 days	Mon 1/1/07	Fri 1/19/07																																																																																																		
260	Detailed Design & Permitting	65 days	Mon 1/22/07	Fri 4/20/07																																																																																																		
261	Advertise & Receive Construction-Contractor Bids	25 days	Mon 4/23/07	Fri 5/25/07																																																																																																		
262	Review Bids/Assoc.Documents, Contract for Construction & Issue NTP	30 days	Mon 5/28/07	Fri 7/6/07																																																																																																		
263	Theater/Fine Arts Facilities Construction	280 days	Mon 7/9/07	Fri 8/1/08																																																																																																		

Project: STBESRT Date: Mon 3/20/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

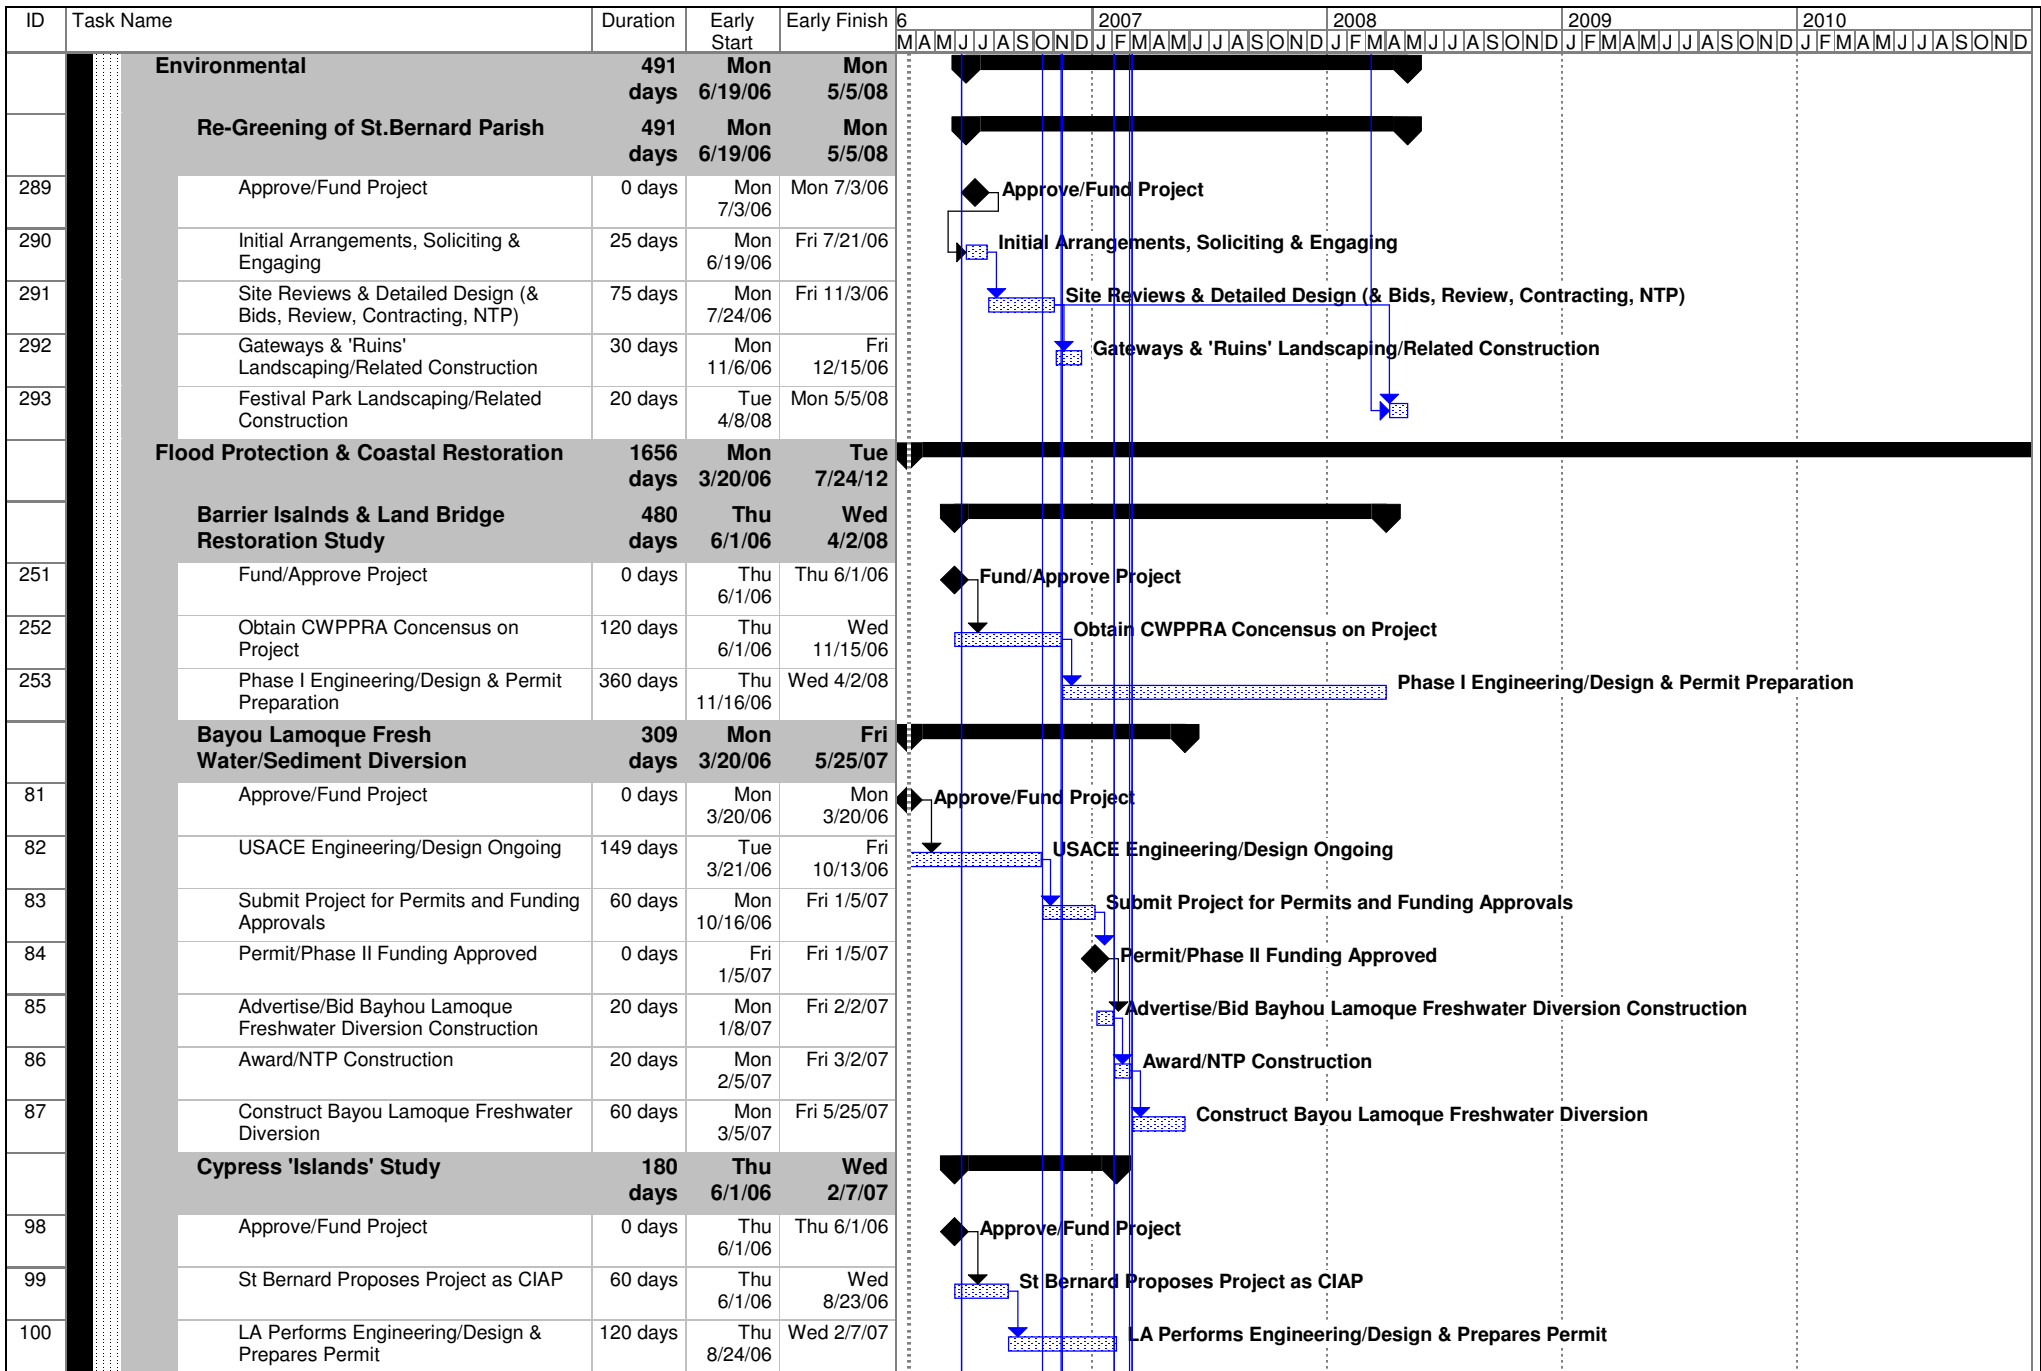


Project: STBESRT Date: Mon 3/20/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

Page 4

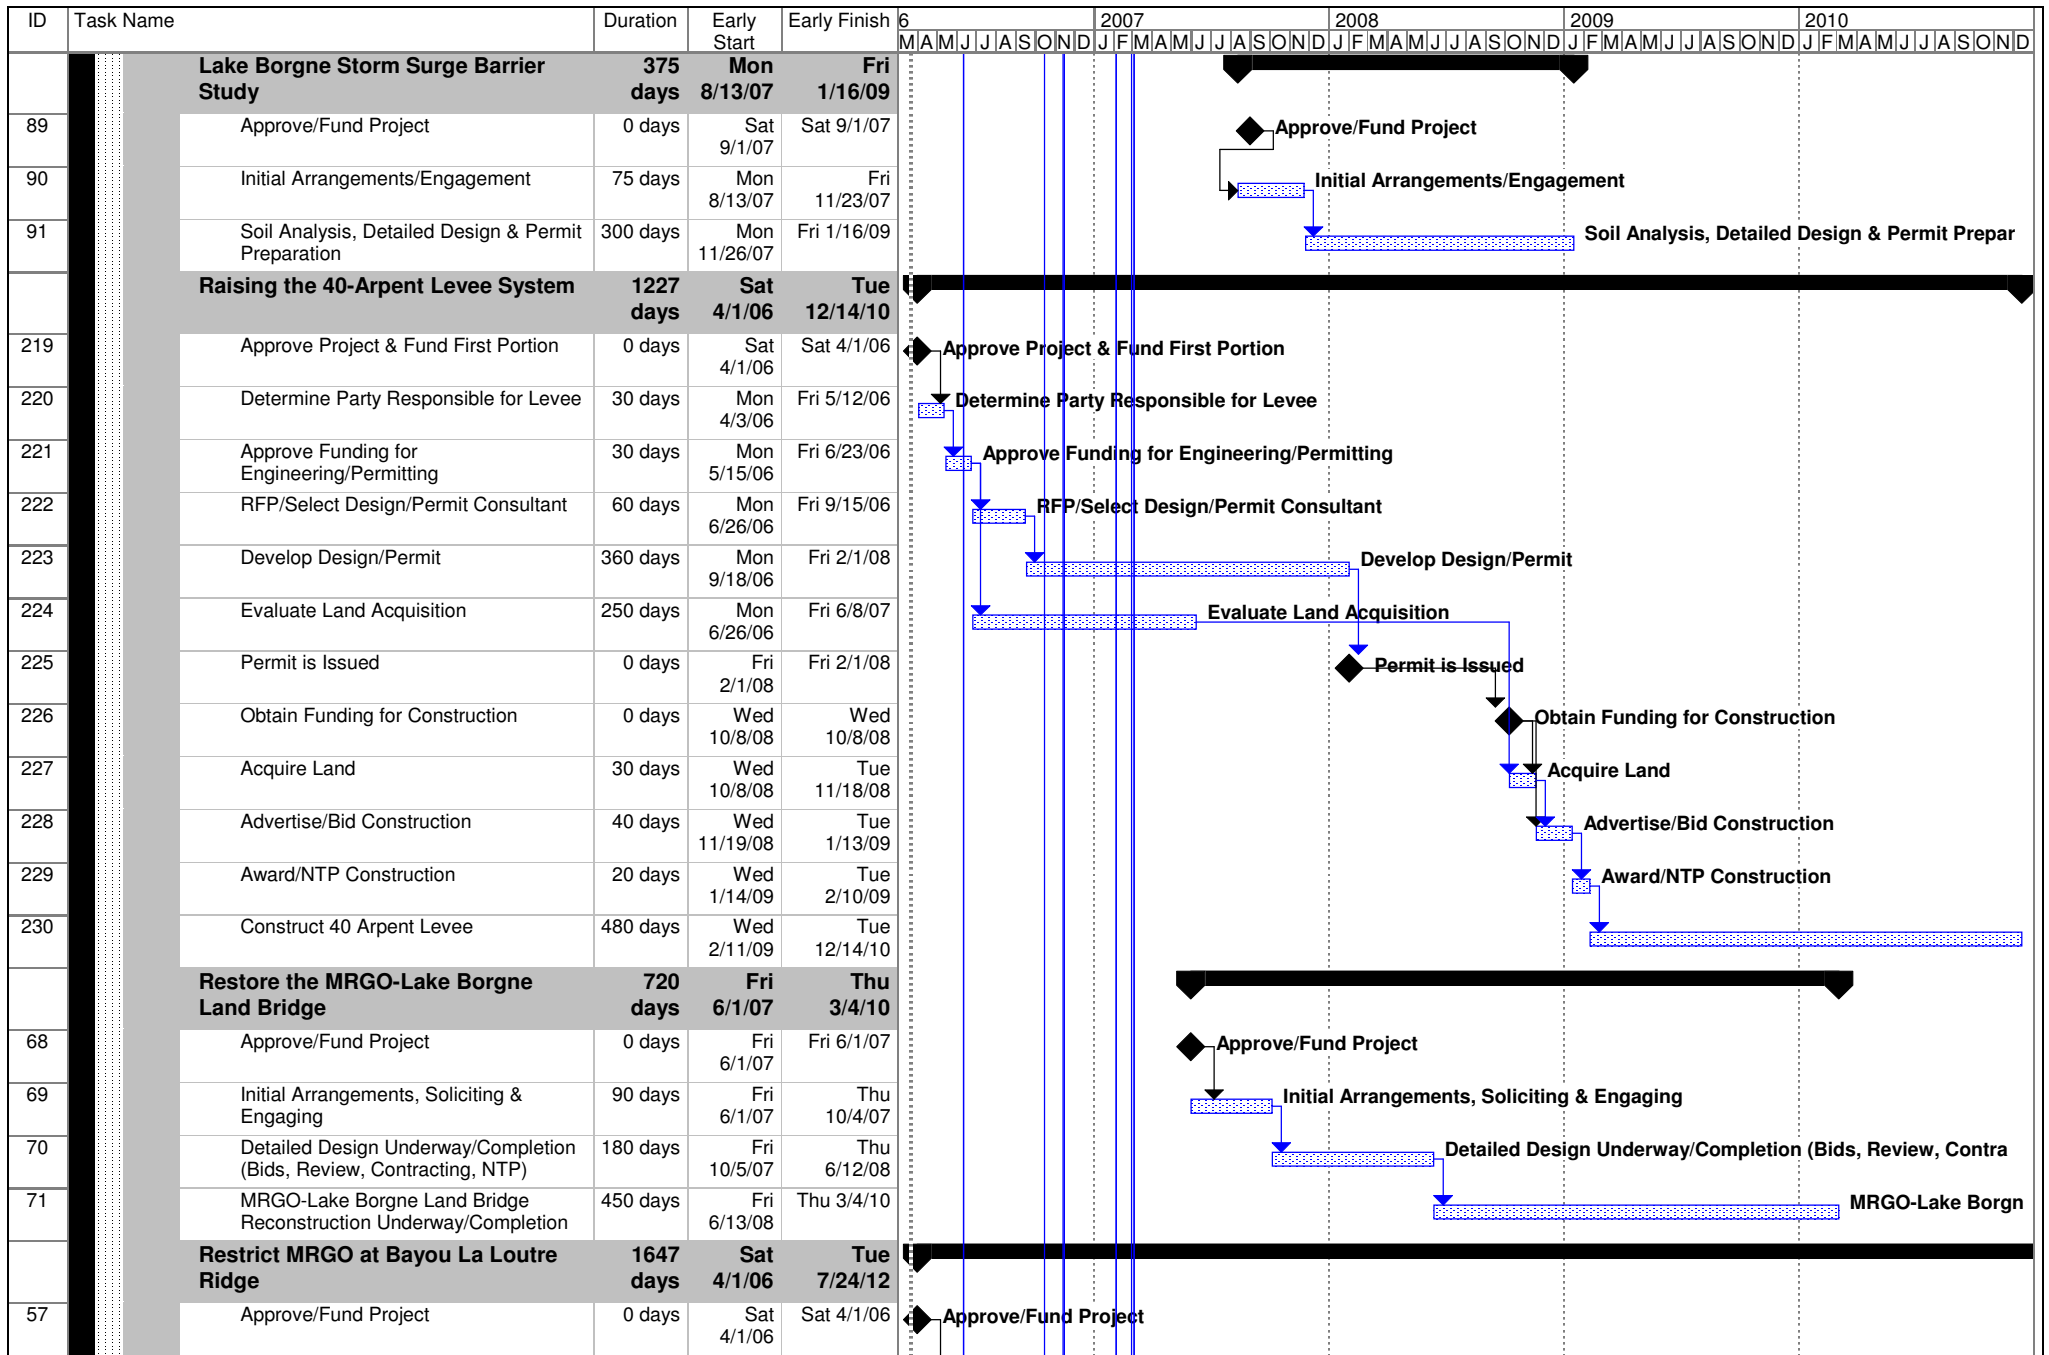

Project: STBESRT Date: Mon 3/20/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

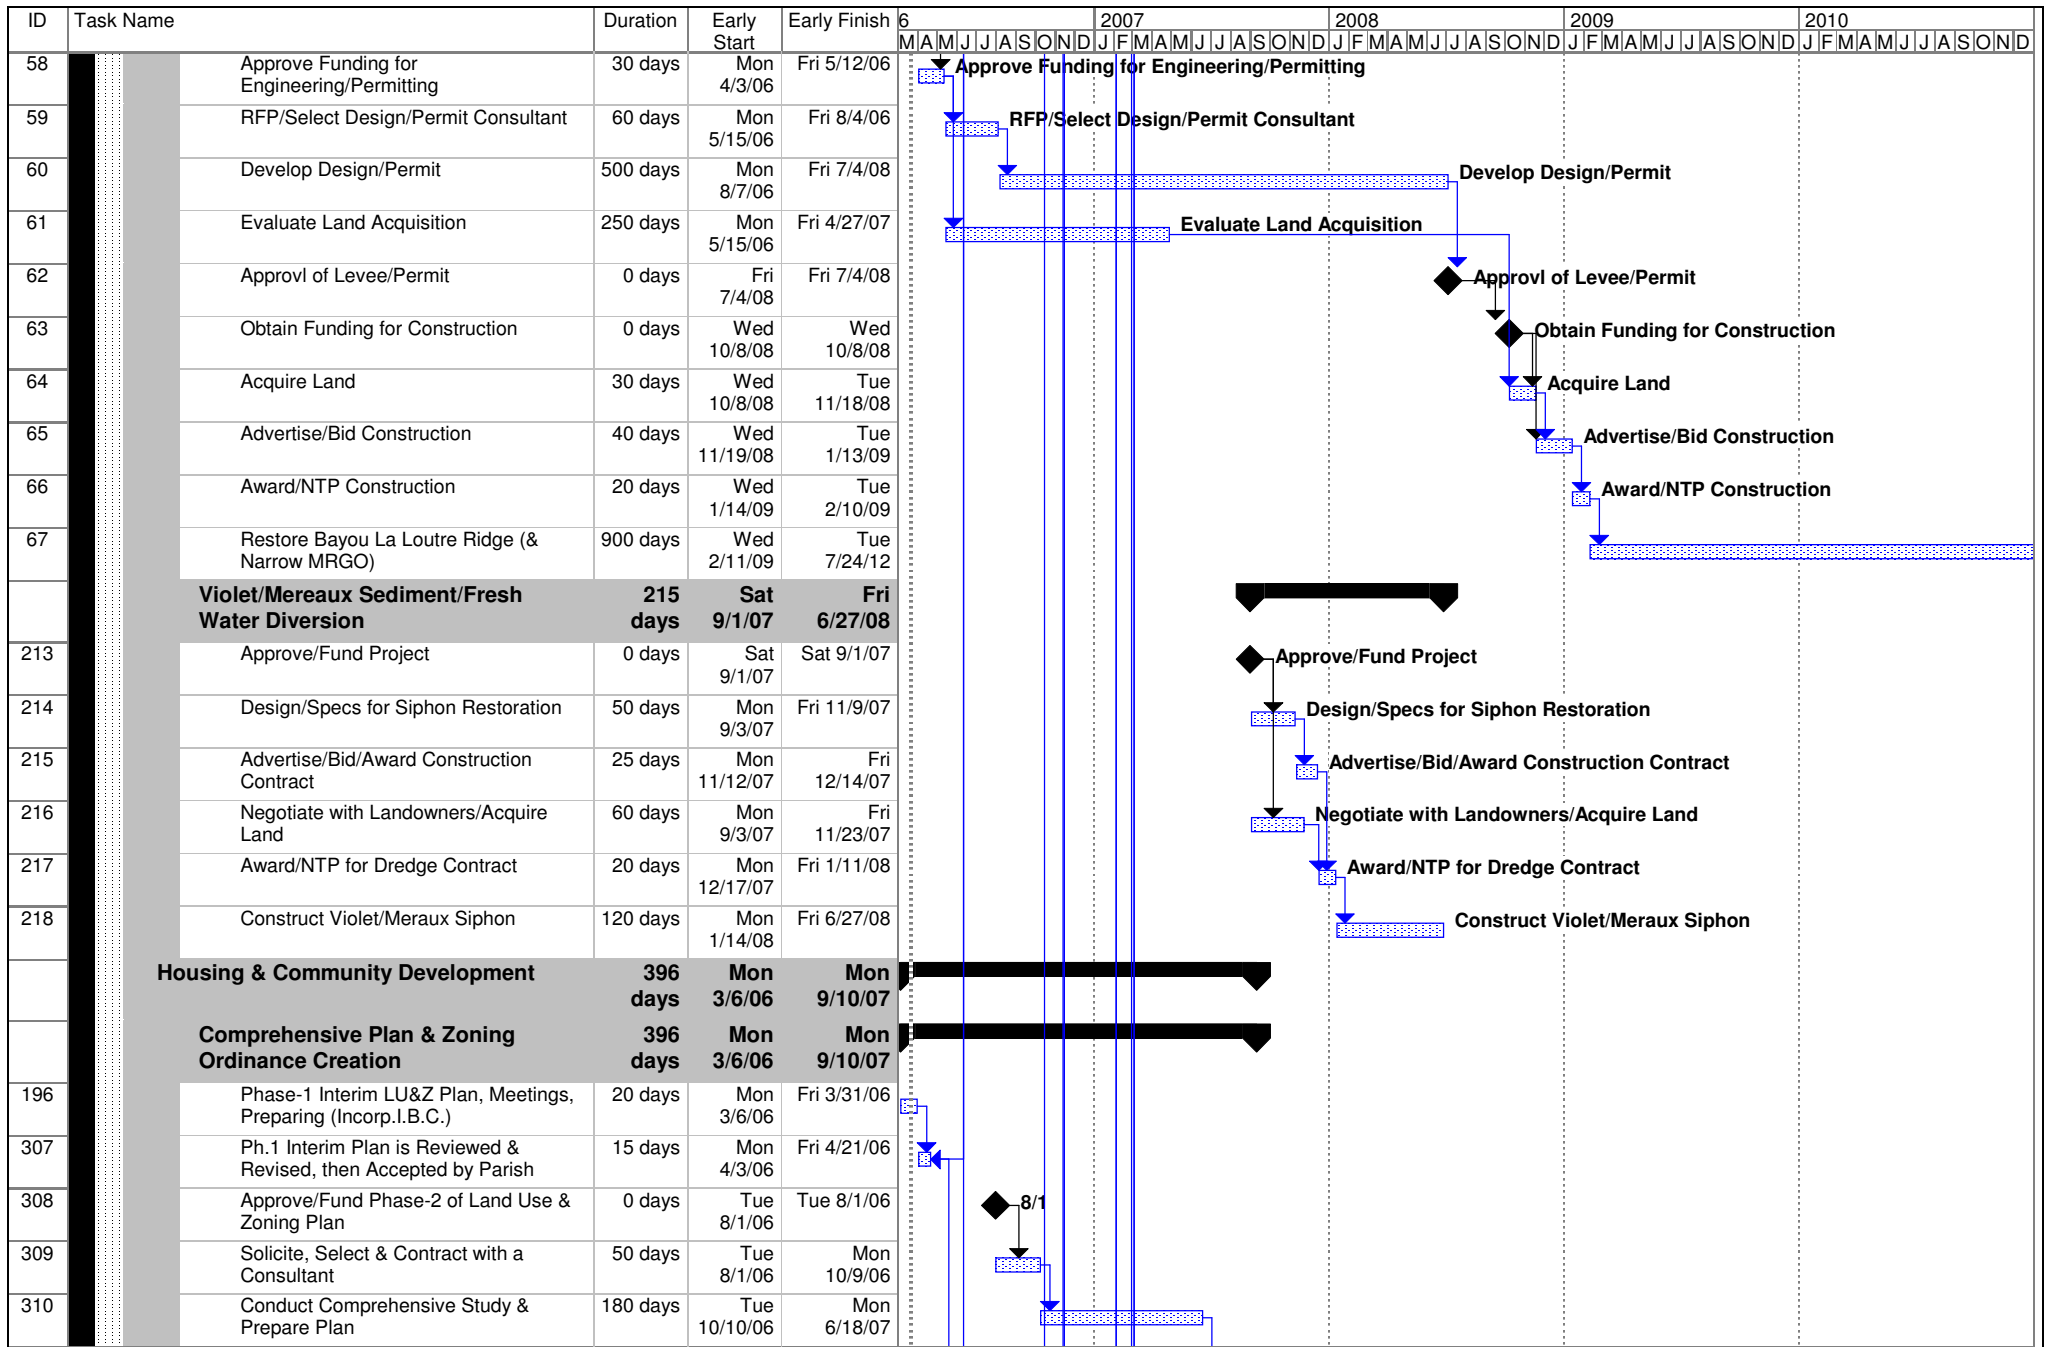


Project: STBESRT Date: Mon 3/20/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	


ID	Task Name	Duration	Early Start	Early Finish	6	2007	2008	2009	2010																																																	
					M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D								
311	Ph.2 Plan is Reviewed & Revised, then Accepted by Parish	60 days	Tue 6/19/07	Mon 9/10/07																																																						
312	Implementation of Comprehensive Plan & Zoning Ordinance Begins	0 days	Mon 9/10/07	Mon 9/10/07																																																						
	Housing Recovery Center	300 days	Mon 4/3/06	Fri 5/25/07																																																						
295	Housing Recovery Center (DRAFT 20MAR06)	300 days	Mon 4/3/06	Fri 5/25/07																																																						
	Human Services	100 days	Mon 5/1/06	Fri 9/15/06																																																						
	Local Capacity Assessment & Staffing Plan	100 days	Mon 5/1/06	Fri 9/15/06																																																						
117	Local Capacity Assessment & Staffing Plan (DRAFT 20MAR06)	100 days	Mon 5/1/06	Fri 9/15/06																																																						
	Public Health & Healthcare	100 days	Mon 5/1/06	Fri 9/15/06																																																						
	New Medical Clinic (Temporary Facility)	100 days	Mon 5/1/06	Fri 9/15/06																																																						
114	Assess South-Central La. Medical Service Needs (DRAFT 20MAR06)	100 days	Mon 5/1/06	Fri 9/15/06																																																						
	Public Safety	932 days	Tue 3/21/06	Wed 10/14/09																																																						
	Public Safety/Emergency Services Complex	932 days	Tue 3/21/06	Wed 10/14/09																																																						
40	Centralized Emergency Command and Control Station	450 days	Tue 3/21/06	Mon 12/10/07																																																						
297	Approve/Fund Project	0 days	Thu 6/1/06	Thu 6/1/06																																																						
298	Issue RFP, Review Proposals, Select & Contract with Designer	75 days	Thu 6/1/06	Wed 9/13/06																																																						
299	Site Investigtn., Environml. Clearance, Land Acquistn. (from Mereaux	90 days	Thu 6/1/06	Wed 10/4/06																																																						
300	Conceptual Design Underway/Completion	50 days	Thu 9/14/06	Wed 11/22/06																																																						
301	Parish Reviews & Officially Accepts (Concept.Design & Site)	30 days	Thu 11/23/06	Wed 1/3/07																																																						
302	Detailed Design Underway/Completion	110 days	Thu 1/4/07	Wed 6/6/07																																																						
303	Obtain Permits	65 days	Thu 3/8/07	Wed 6/6/07																																																						
304	Advertise & Receive Construction/Contractor Bids	35 days	Thu 6/7/07	Wed 7/25/07																																																						
305	Review Bids/Assoc. Documents, Contract for Construction & Issue NTP	40 days	Thu 7/26/07	Wed 9/19/07																																																						
306	Safety/Emergency Complex Construction	540 days	Thu 9/20/07	Wed 10/14/09																																																						

Project: STBESRT
Date: Mon 3/20/06

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

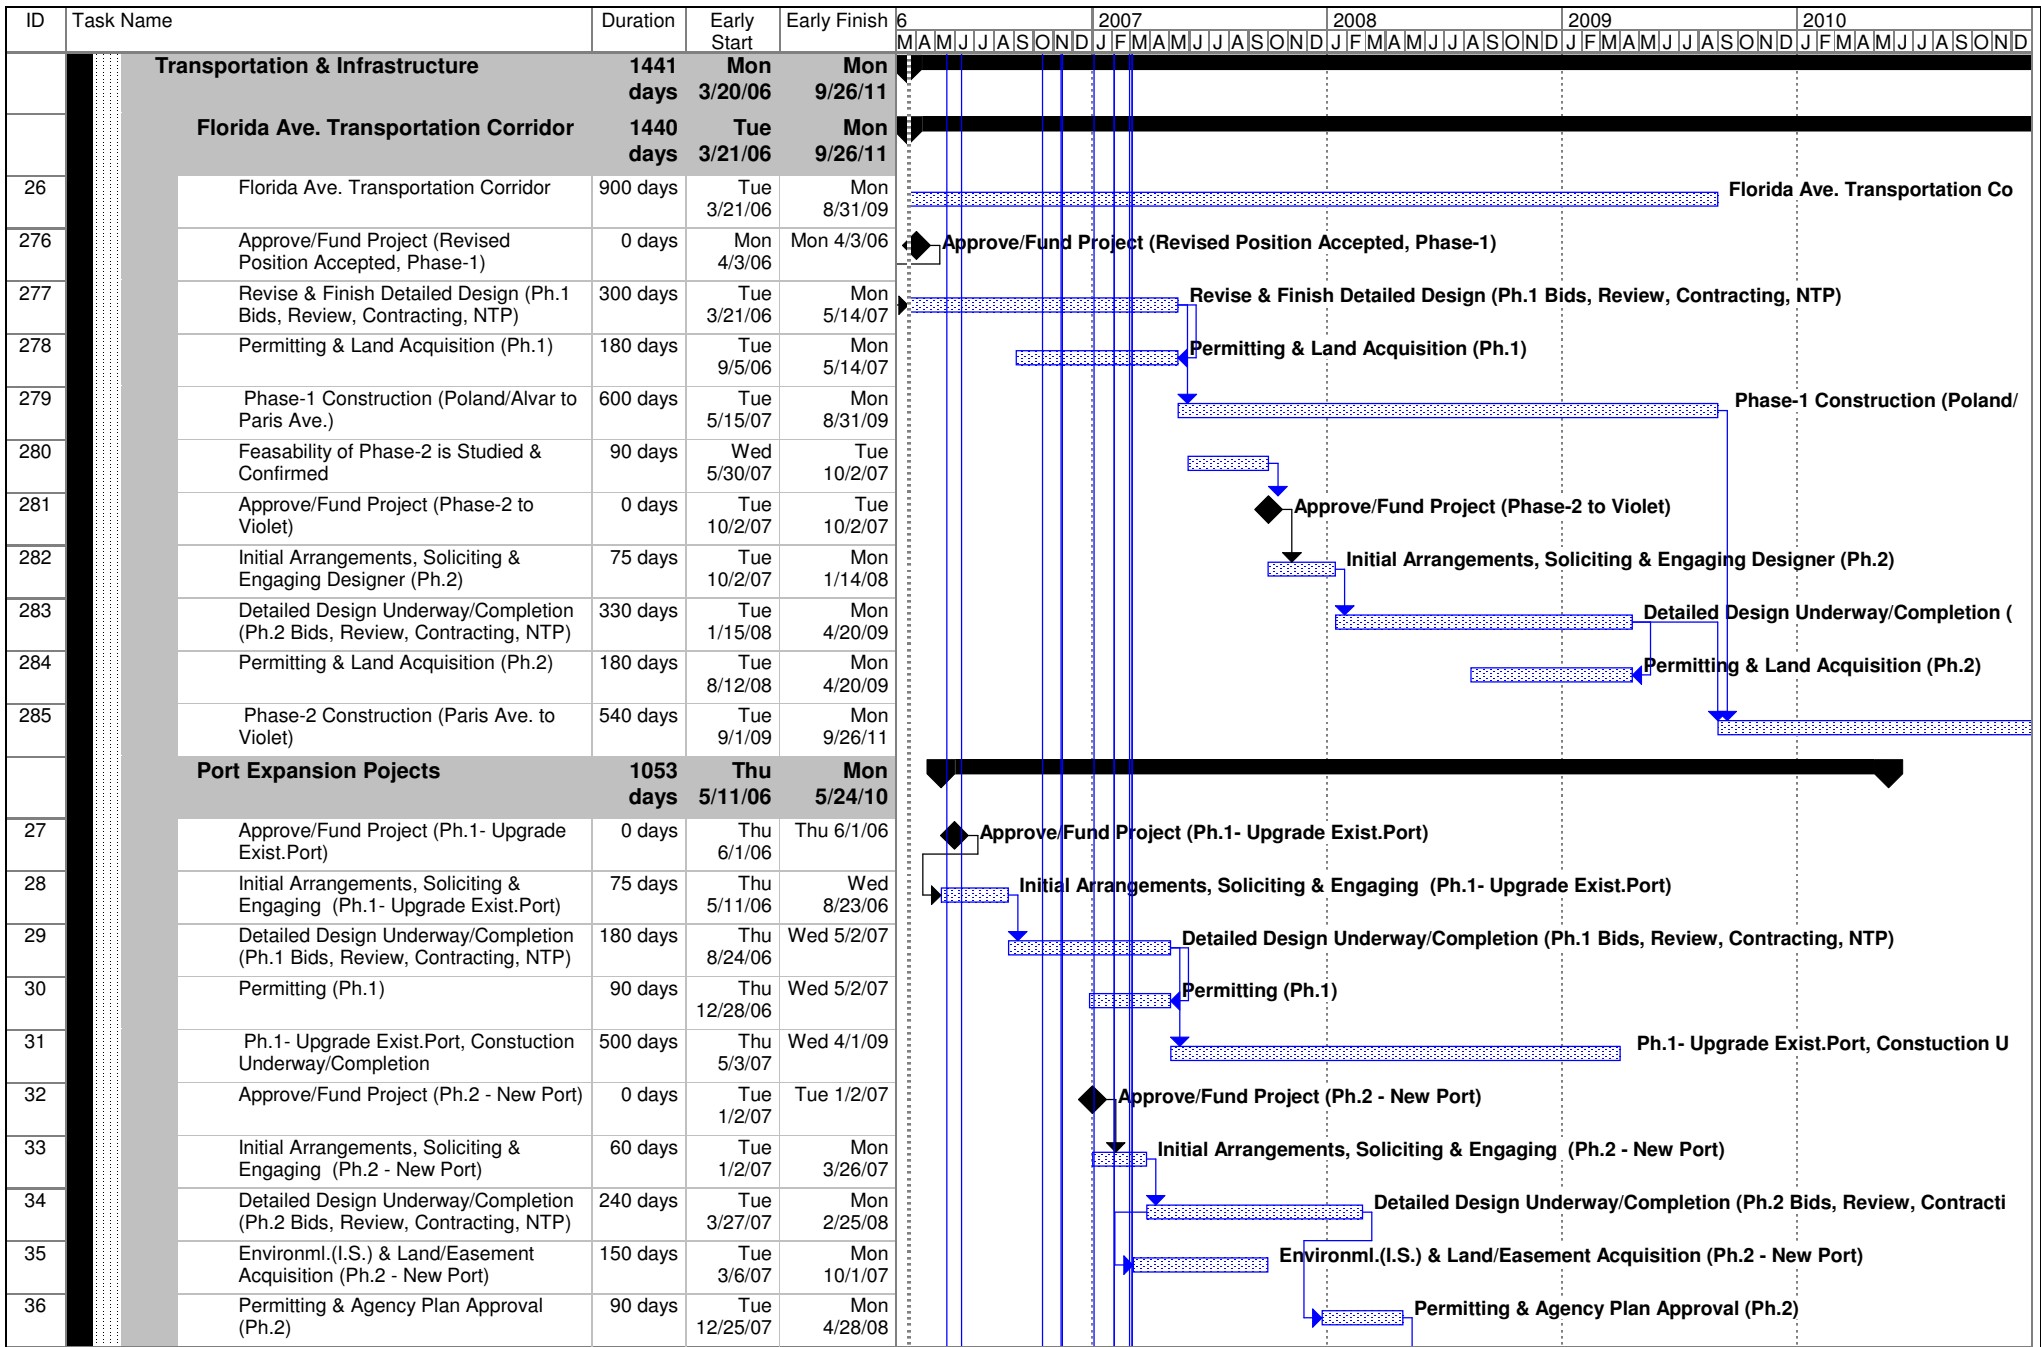

Project: STBESRT Date: Mon 3/20/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

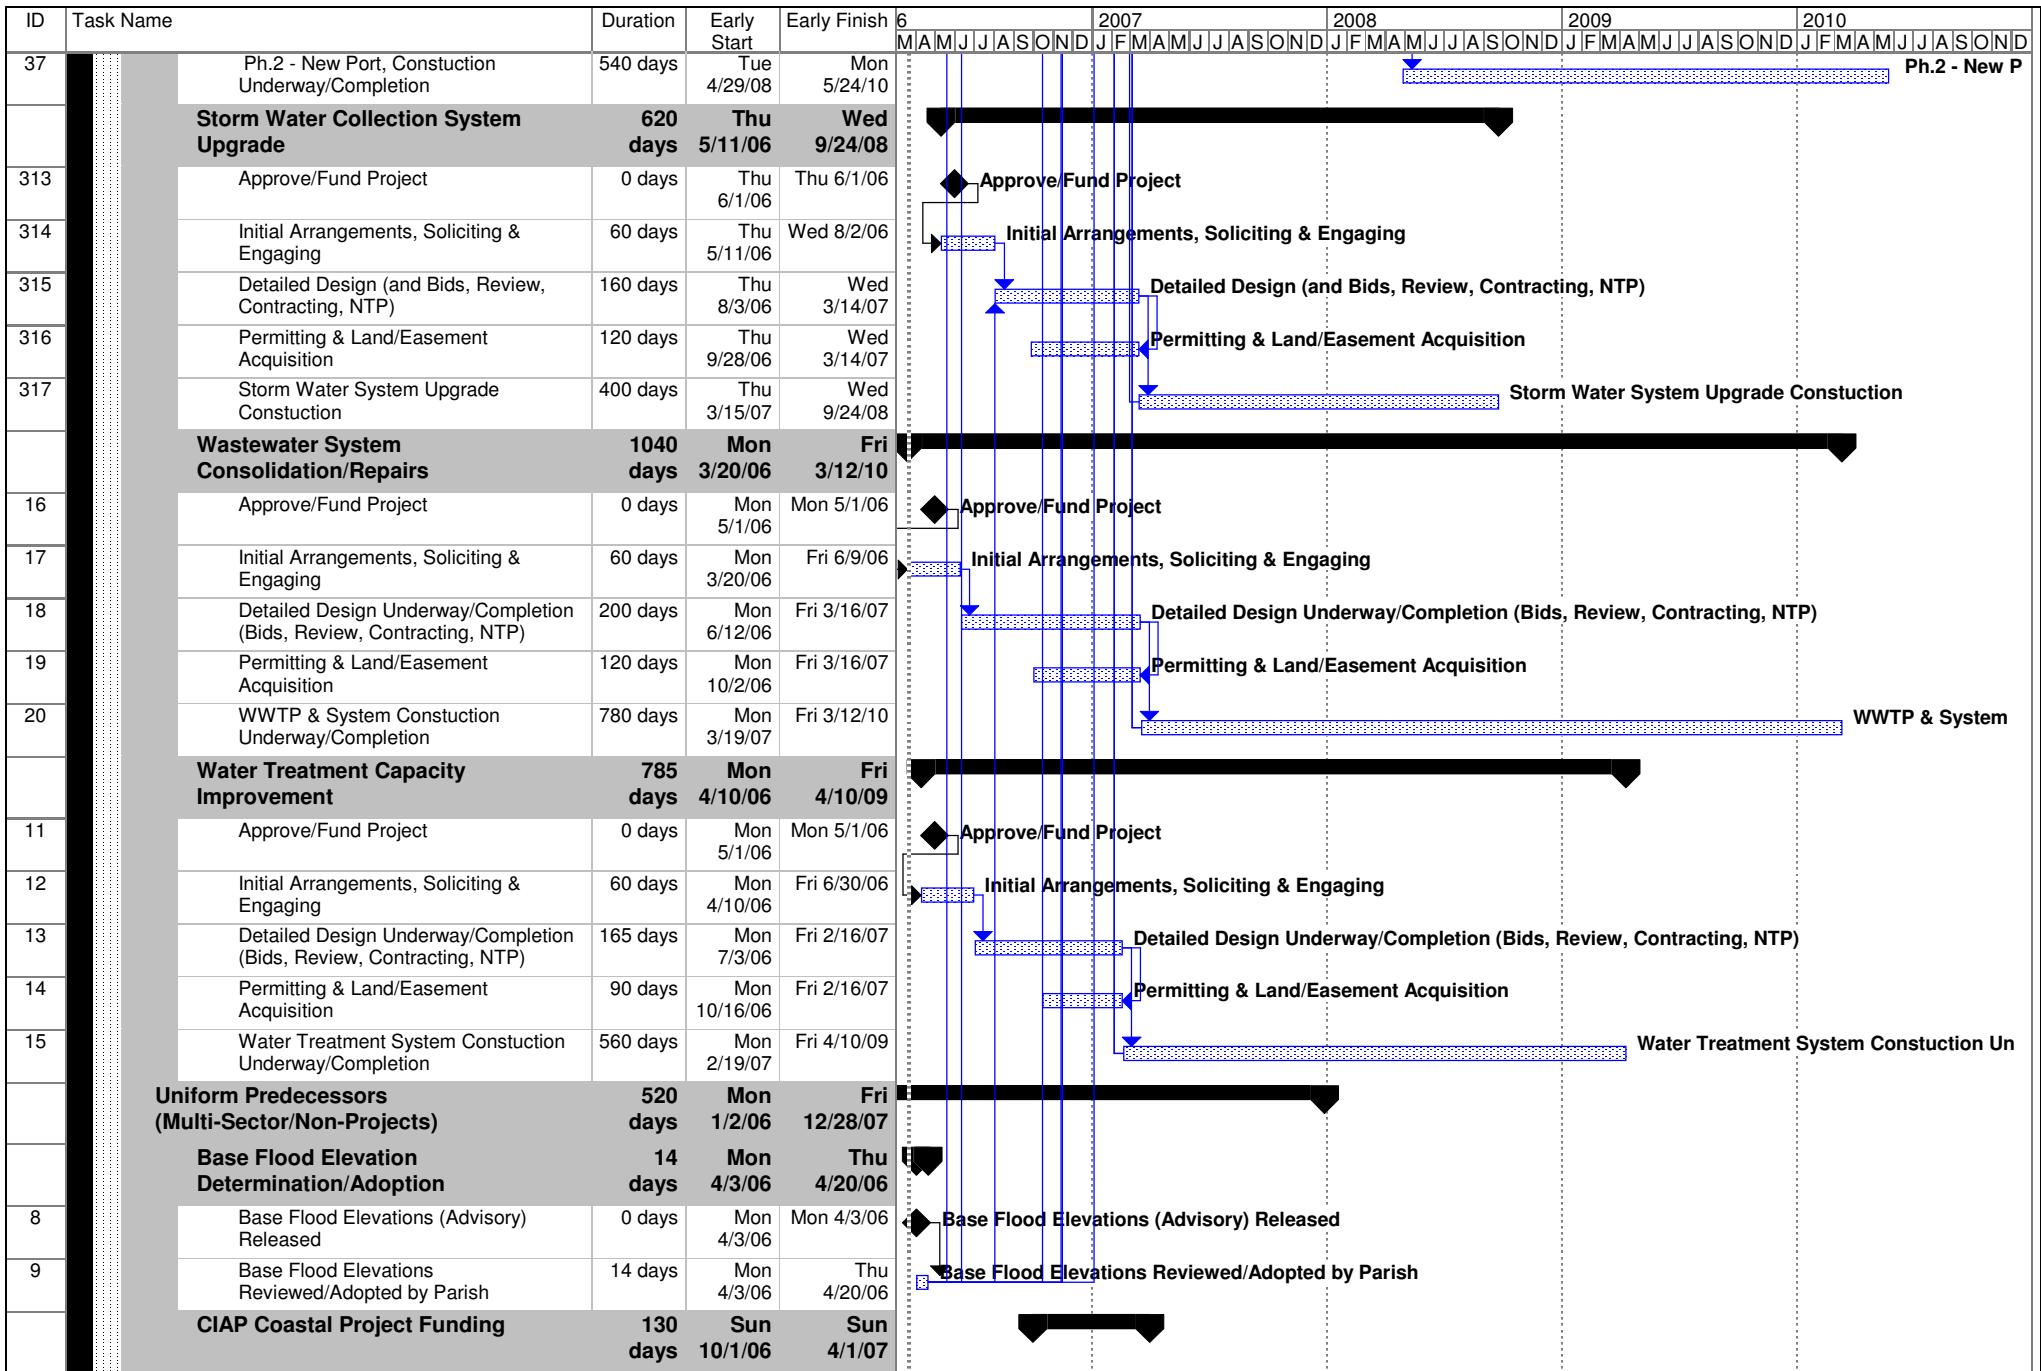

Project: STBESRT Date: Mon 3/20/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

